



Construction Progress by DiMeo Bros, Inc. (DiMeo)




	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

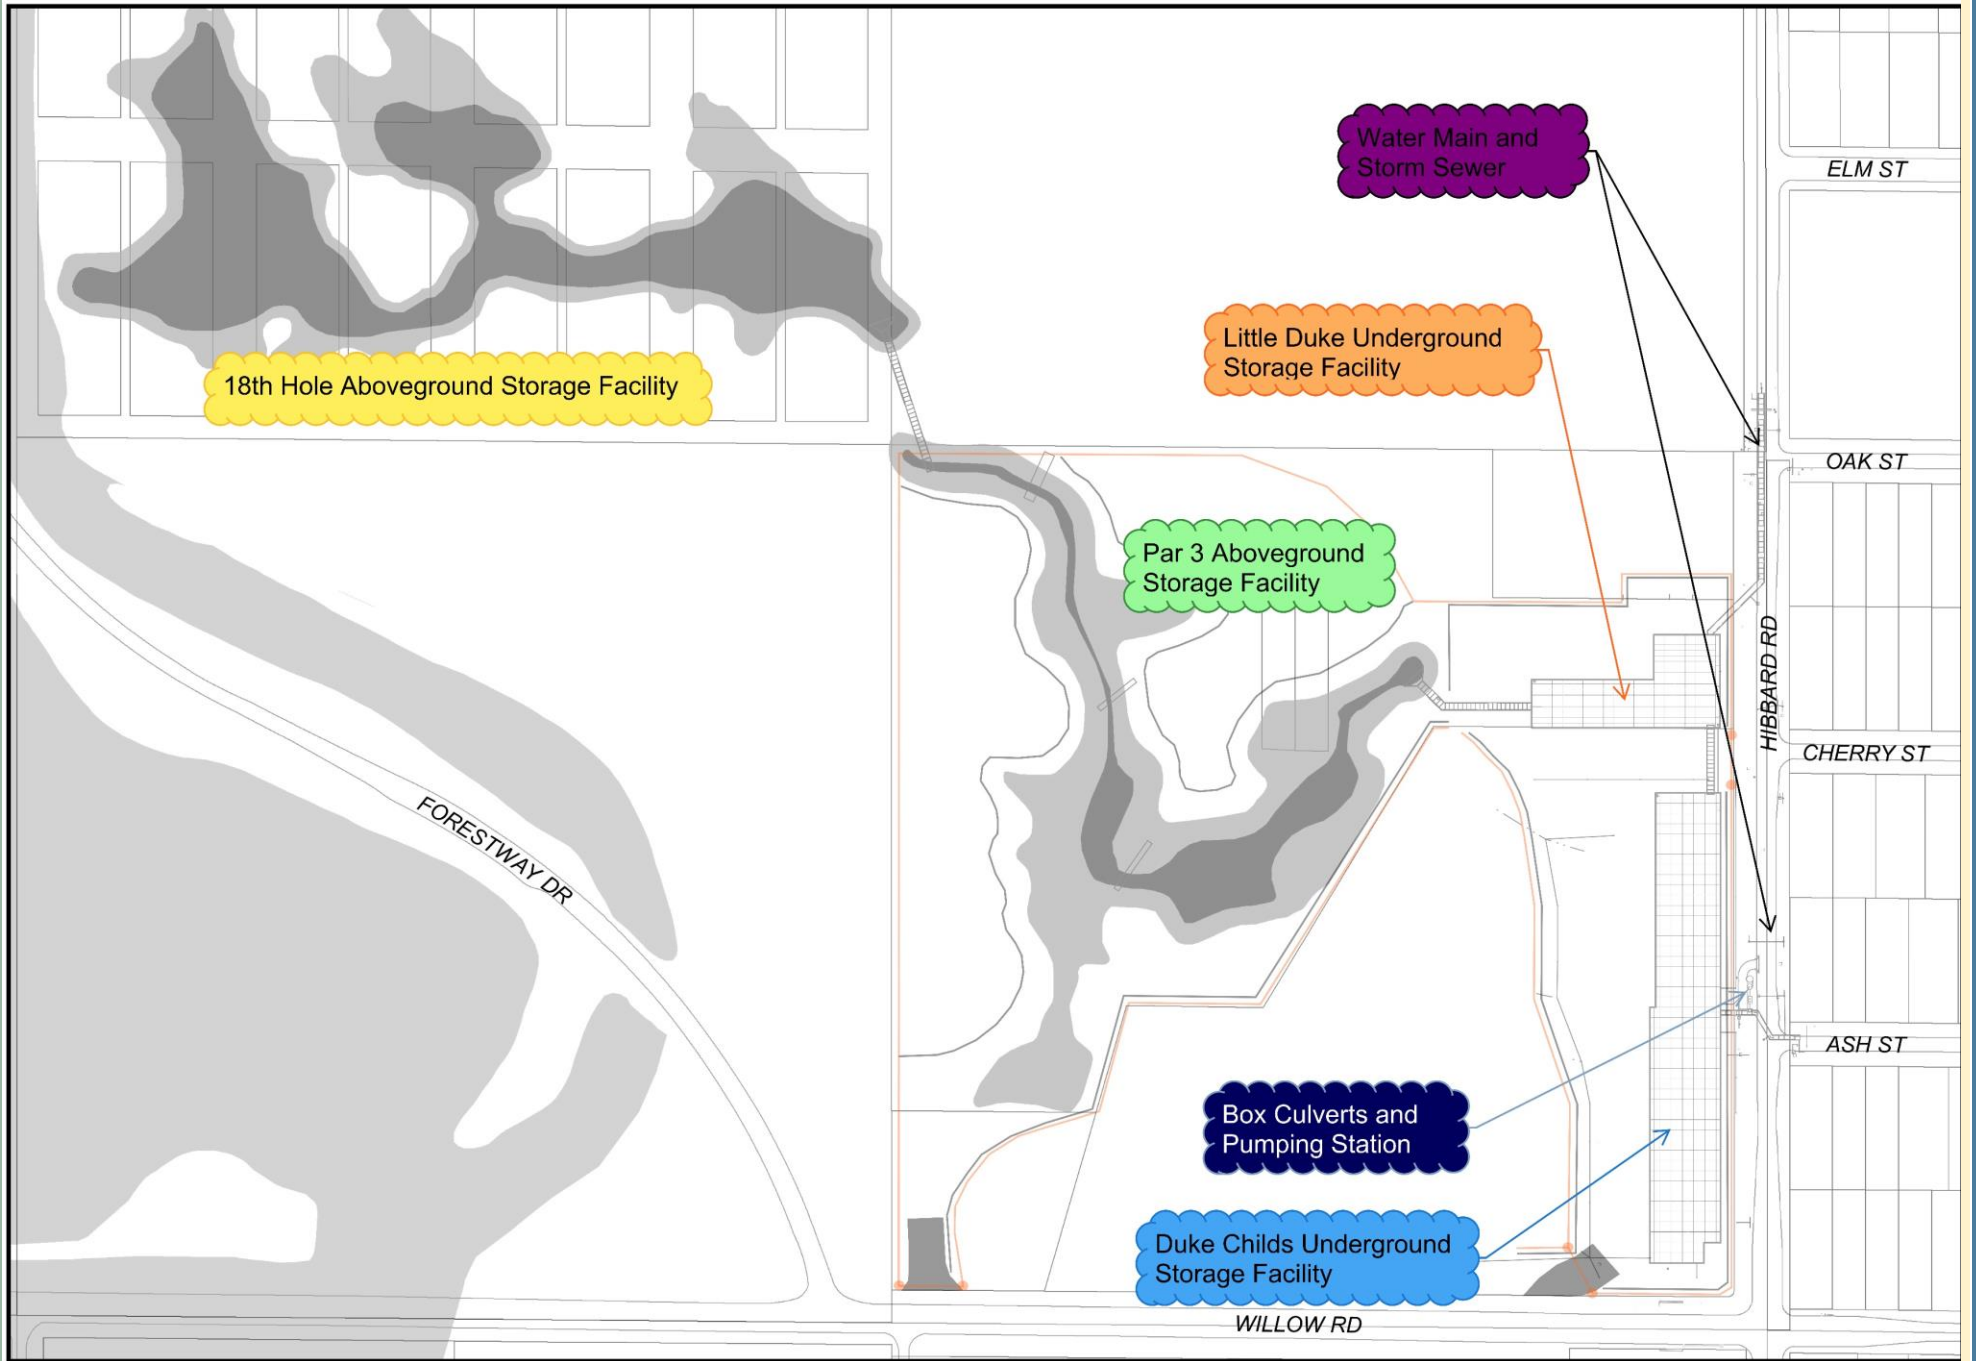

DiMeo widened the roadway leading to the landfill for improved traffic flow.

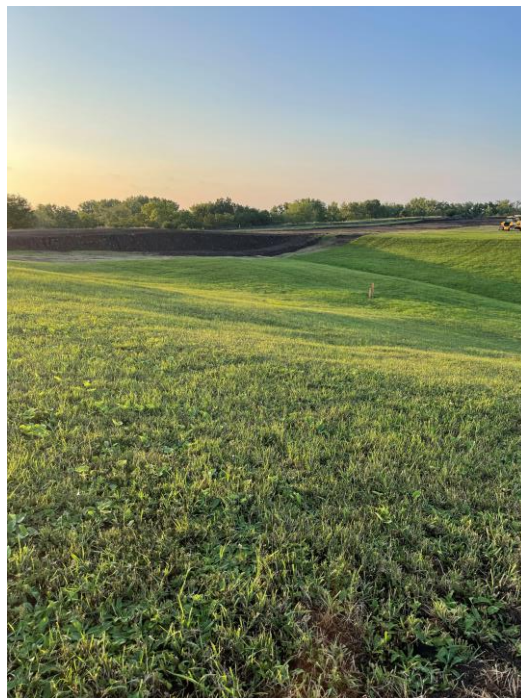

Topsoil was stripped and stockpiled on top of the landfill.

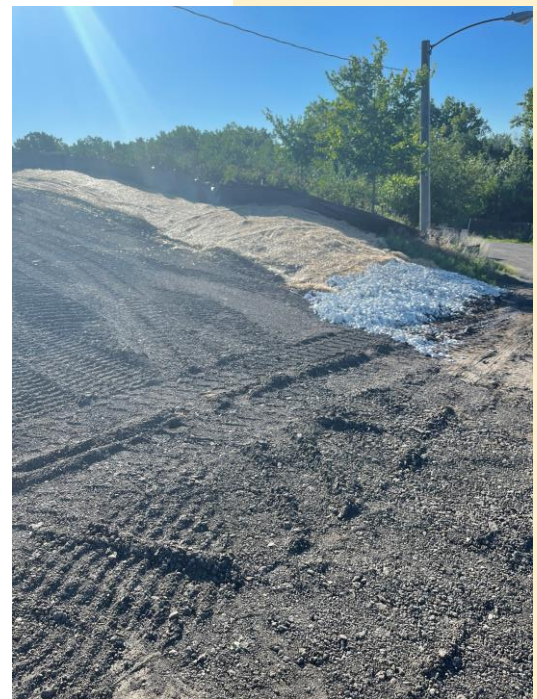

Riprap, asphalt grindings, and silt fence make for a sturdier route for disposal of earth on the landfill.

WORK THIS WEEK (week of 8/29/2022)

- DiMeo began stripping and stockpiling topsoil on top of the landfill in preparation for receiving excavated earth from the Par 3 Course
- DiMeo improved the route through the Village Public Works Facility up to the landfill to make for better traffic flow
- Sprinkler heads on the Par 3 Course were removed and stored away ahead of excavation

WORK NEXT WEEK (week of 9/5/2022)

- DiMeo will begin to excavate out the Par 3 Storage Facility
- Traffic control on Willow Road will begin to allow for movement of truck traffic between the Par 3 Course and the landfill. Please be safe if you are driving in this area!

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

