


Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

WILLOW ROAD TRAFFIC NOTICE: Excavated soils will continue to be trucked across Willow Road causing temporary traffic congestion and increased travel times. Additionally, StormTrap underground units will be delivered onsite via Willow Road. Please consider using alternate routes.

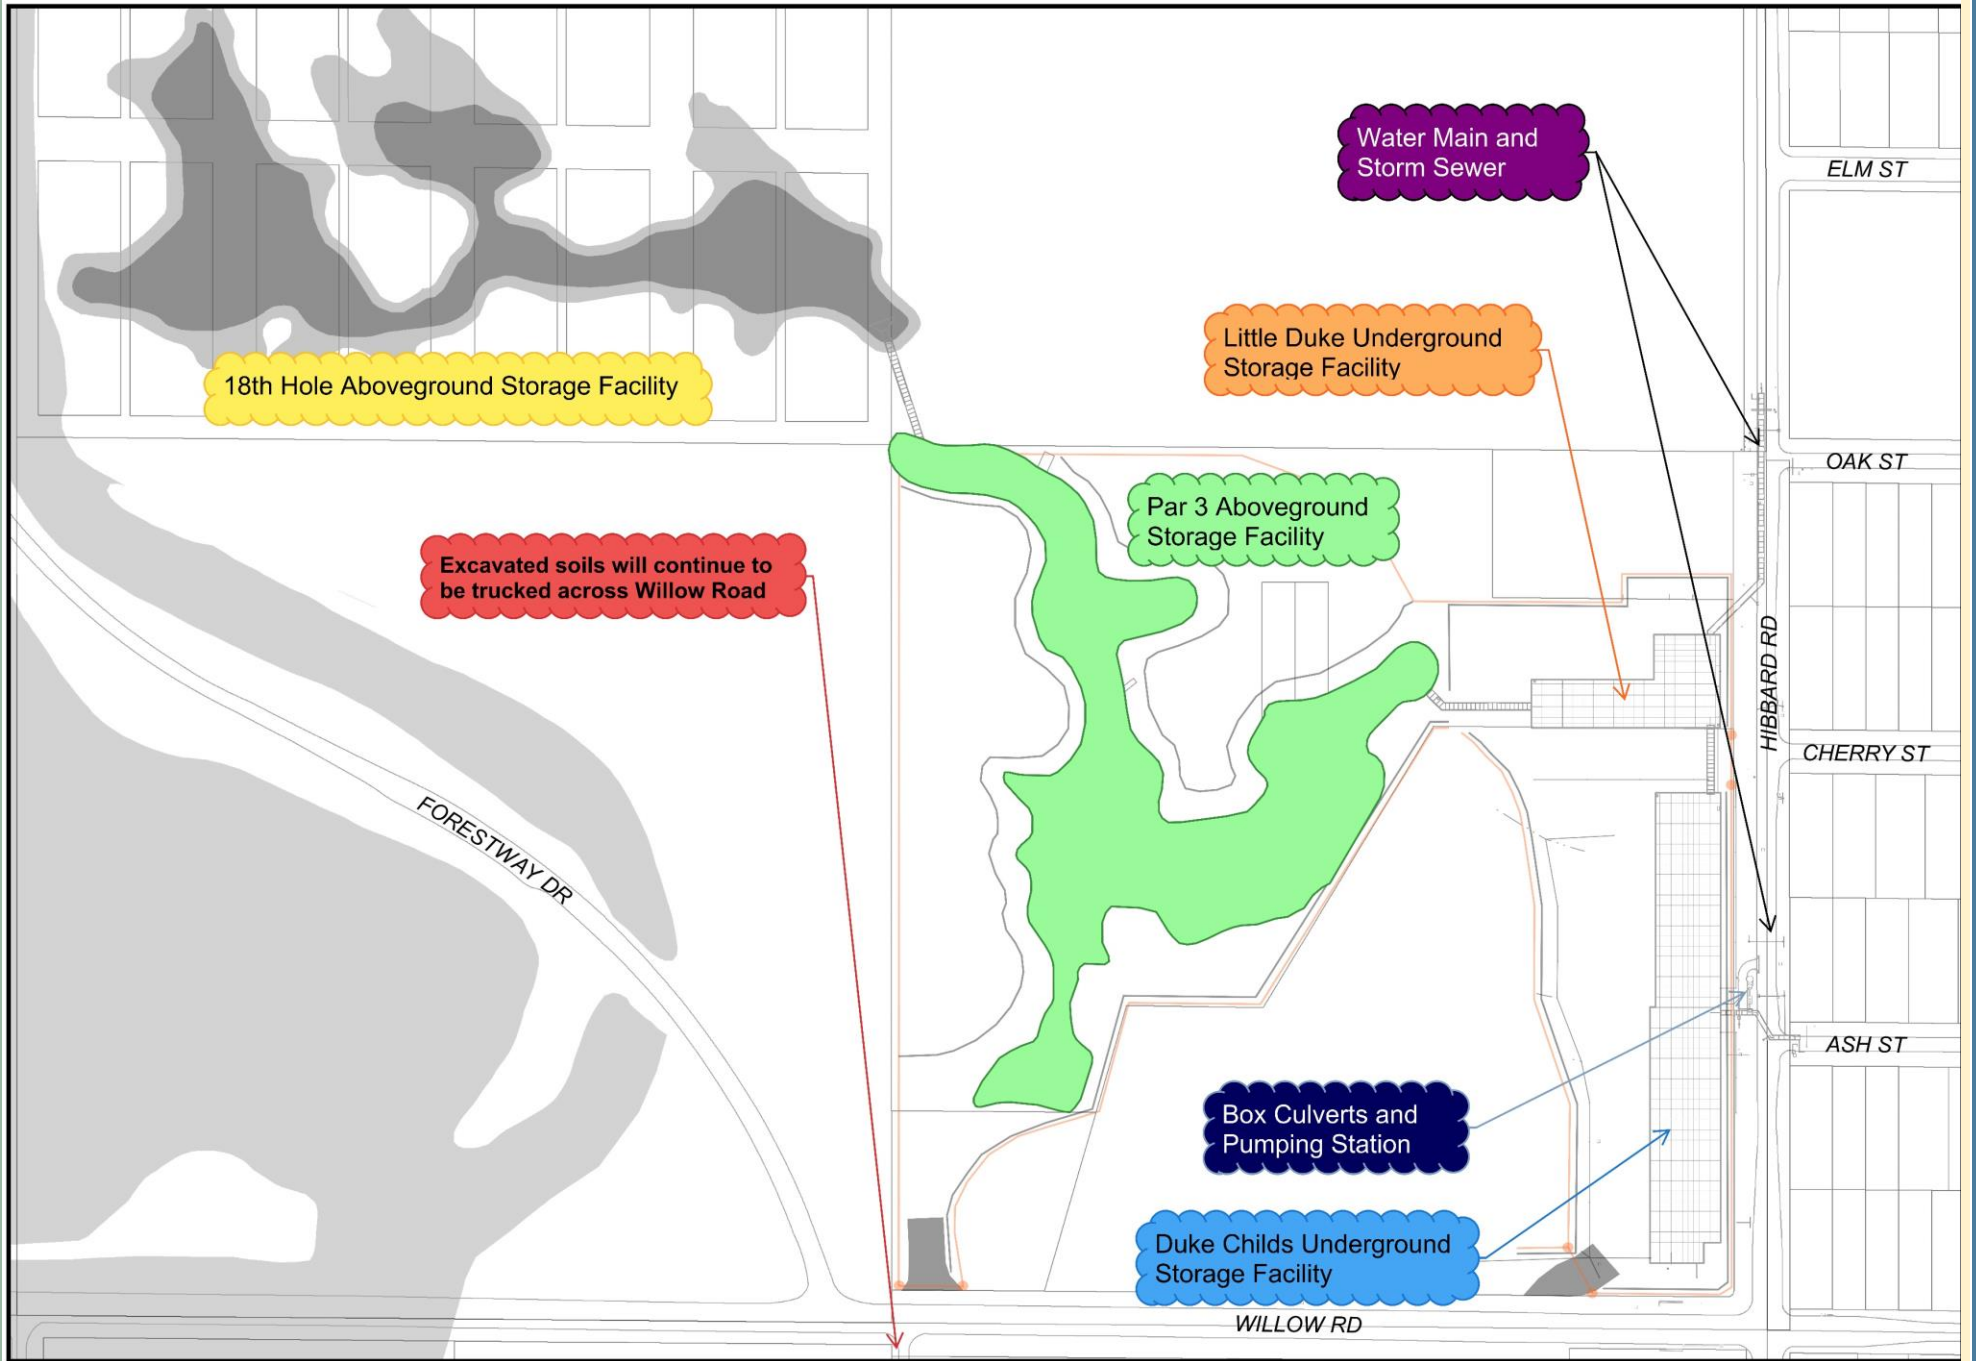

The last part of the Par 3 Storage Facility was excavated this week



DiMeo began scraping topsoil off Duke Childs Field

WORK THIS WEEK (week of 10/10/2022)

- The Par 3 Storage Facility is complete! Over 45,000 cubic yards of earth has been excavated to create stormwater storage
- DiMeo will now stabilize all the Par 3 Storage Facility with turf reinforcement mat, erosion control blanket, topsoil, and seed
- DiMeo began scraping topsoil off Duke Childs and Little Duke Fields

WORK NEXT WEEK (week of 10/17/2022)

- DiMeo will continue restoration of the Par 3 Storage Facility
- Excavation of the Duke Childs Underground Storage Facility will commence! Delivery of the StormTrap units will also begin next week

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

