


Construction Progress by DiMeo Bros, Inc. (DiMeo)



| | Jul-22 | Aug-22 | Sep-22 | Oct-22 | Nov-22 | Dec-22 | Jan-23 | Feb-23 | Mar-23 | Apr-23 | May-23 | Jun-23 | Jul-23 | Aug-23 | Sep-23 |
|--|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|
| Par 3 Aboveground Storage Facility | | | | | | | | | | | | | | | |
| 18th Hole Aboveground Storage Facility | | | | | | | | | | | | | | | |
| Duke Childs Underground Storage Facility | | | | | | | | | | | | | | | |
| Little Duke Underground Storage Facility | | | | | | | | | | | | | | | |
| Hibbard Road Closure | | | | | | | | | | | | | | | |
| Water Main and Storm Sewer | | | | | | | | | | | | | | | |
| Box Culverts and Pumping Station | | | | | | | | | | | | | | | |
| Golf Course and Little Duke Restoration | | | | | | | | | | | | | | | |


WILLOW ROAD TRAFFIC NOTICE: Excavated soils will continue to be trucked across Willow Road causing temporary traffic congestion and increased travel times. Additionally, StormTrap underground units will be delivered onsite via Willow Road. Please consider using alternate routes.

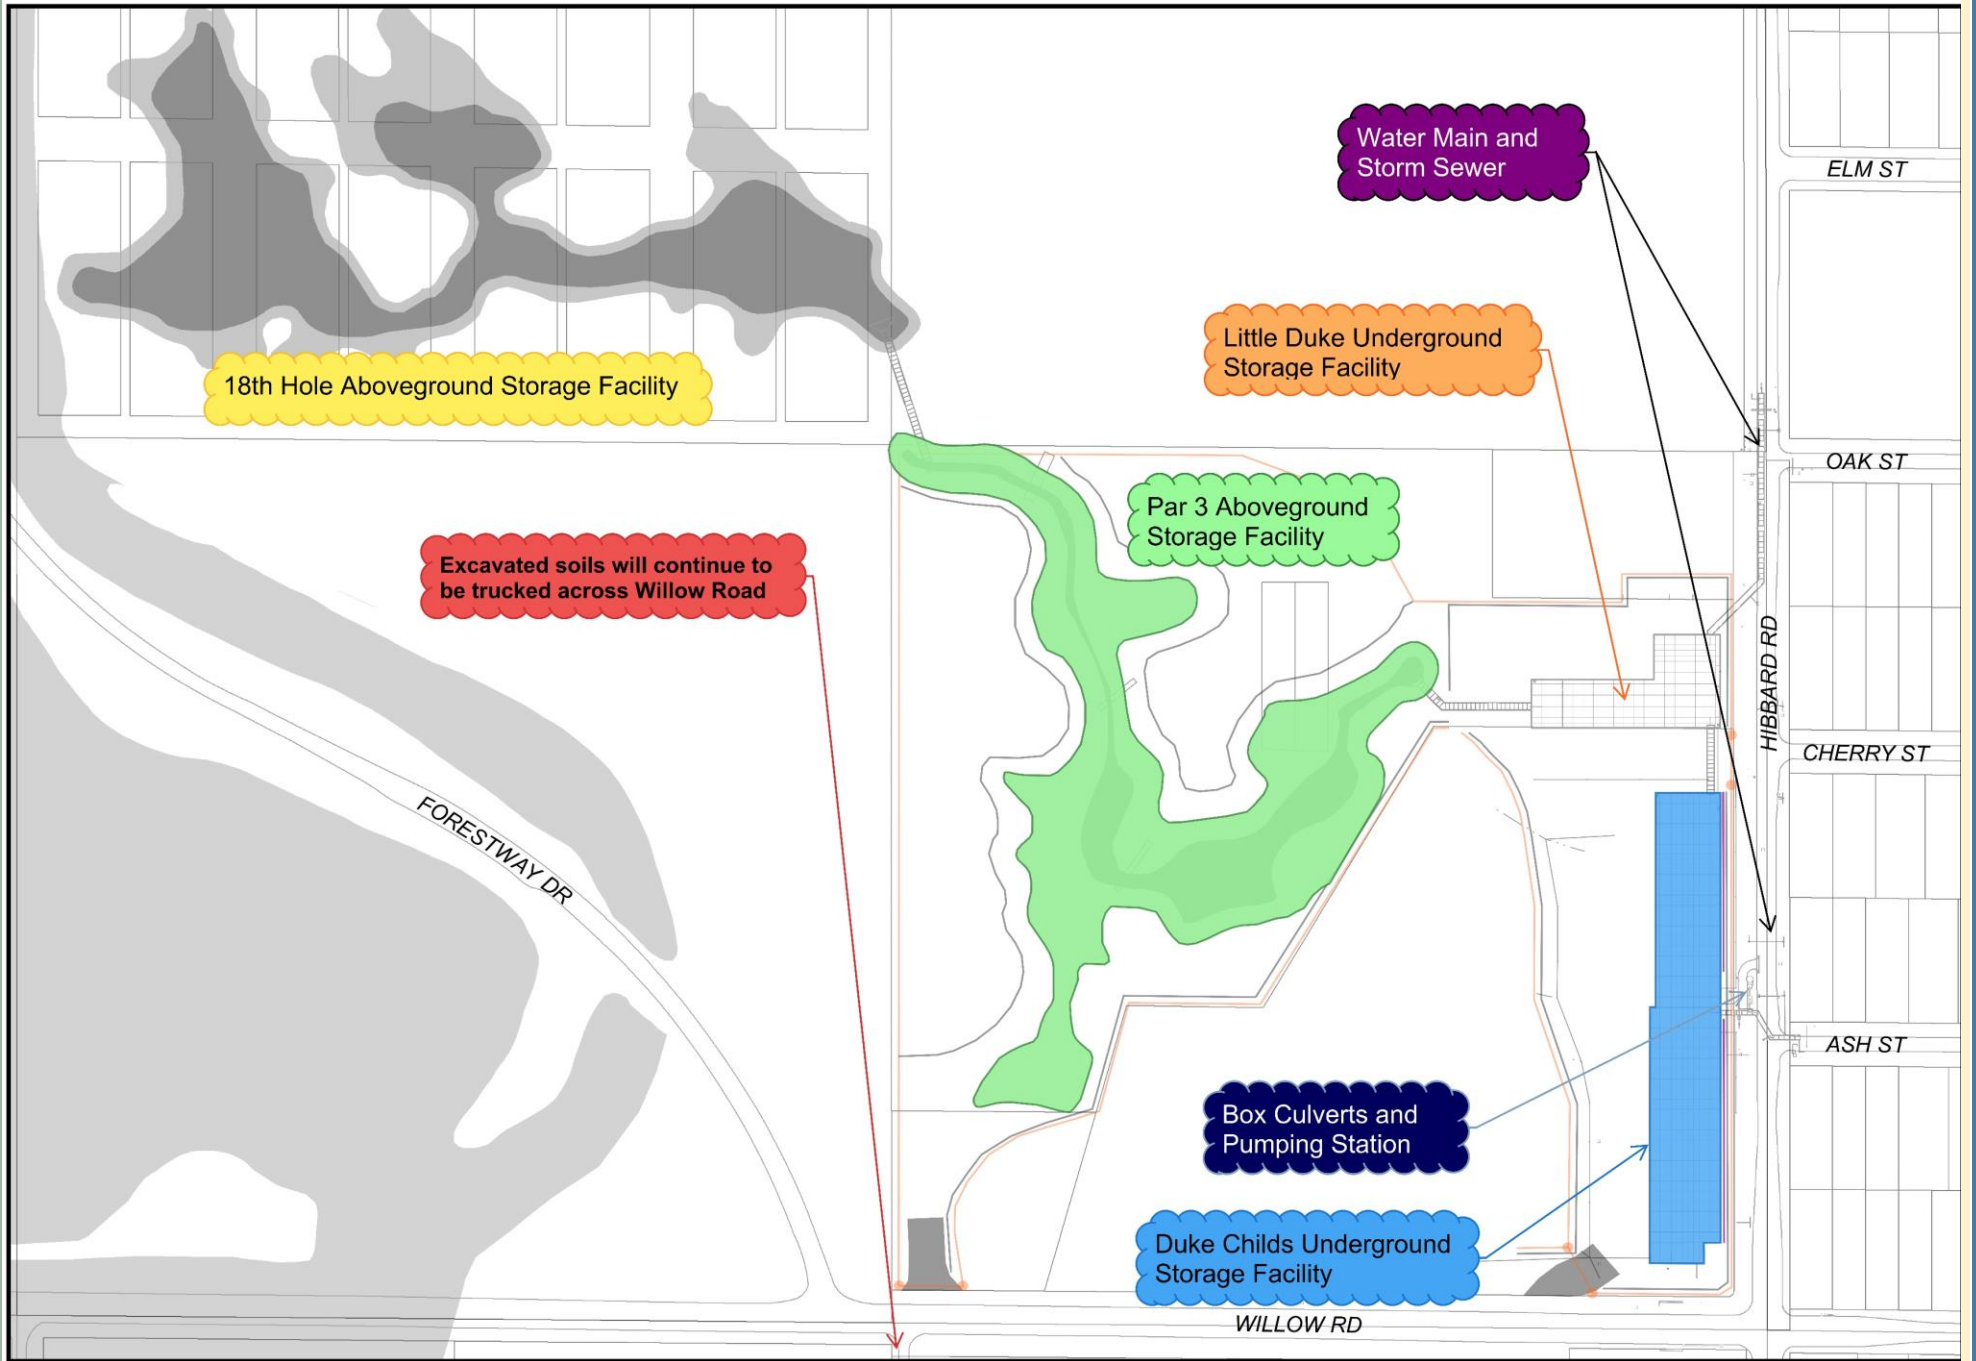

The Duke Childs Underground Storage Facility stands at nearly 10 feet tall



Delivery of storm sewer pipe to the 18 Hole Course began this week

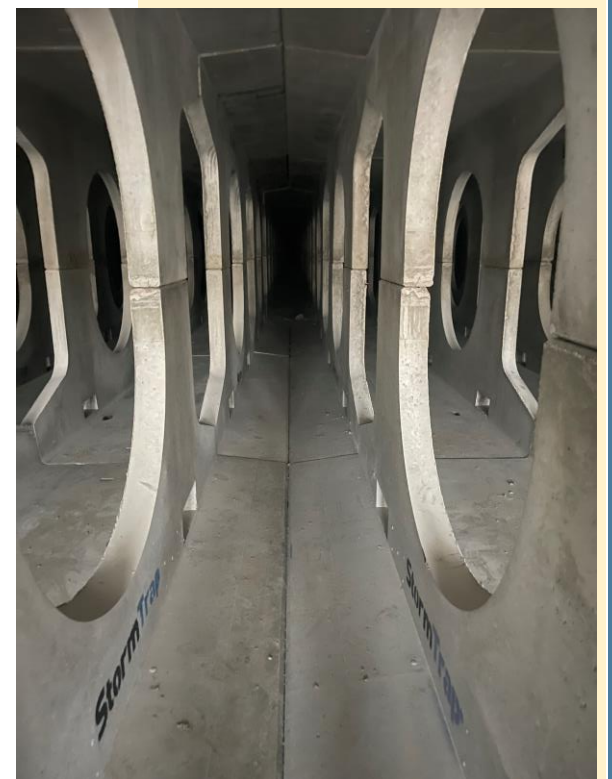

StormTrap installation on Duke Childs Field is complete!

WORK THIS WEEK (week of 11/7/2022)

- DiMeo is finished with installing the Duke Childs Underground Storage Facility!
- DiMeo has also installed about 440 feet of storm sewer force main adjacent to the Duke Childs Storage Facility
- Erosion controls, orange construction fence, and storm sewer pipe began to be delivered to the 18 Hole Course

WORK NEXT WEEK (week of 11/14/2022)

- DiMeo will begin installation of the Little Duke Storage Facility. Delivery of the StormTrap units will continue to use Willow Road for the next several weeks
- The 18 Hole Course at Winnetka Golf Club will continue to see orange construction fence and erosion control installation
- DiMeo will begin installing a 36" storm sewer overflow pipe in the 18 Hole Course. After that is installed, excavation can begin

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

