


Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

WILLOW ROAD TRAFFIC NOTICE: Excavated soils will continue to be trucked across Willow Road causing temporary traffic congestion and increased travel times. Also, StormTrap underground units will be delivered onsite via Willow Road. Please consider using alternate routes and respect flaggers.

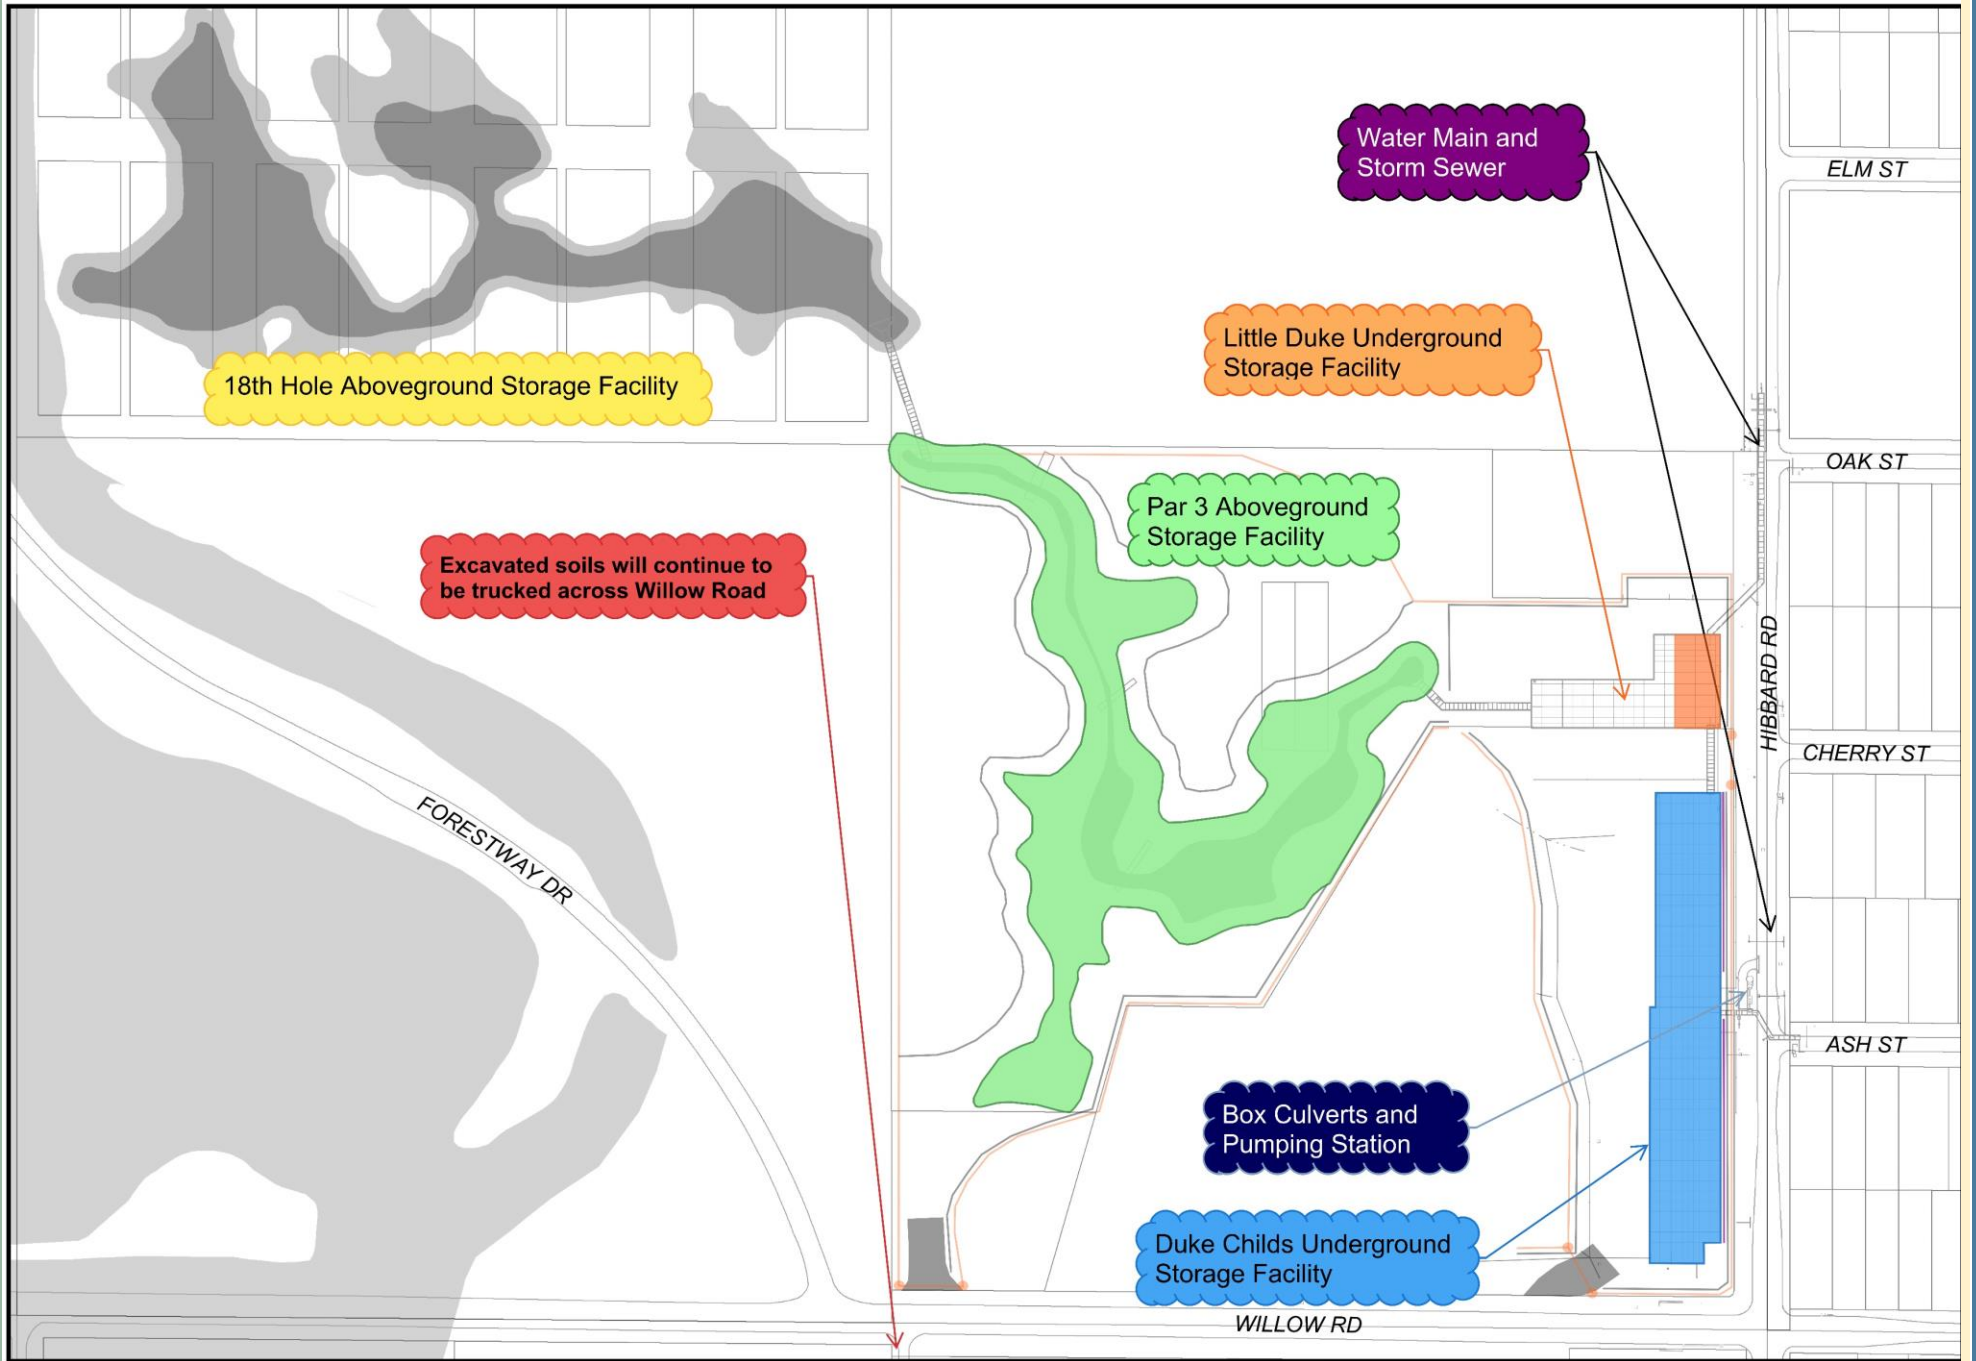

Little Duke StormTrap installation began in earnest



The 18 Hole Course overflow storm sewer began installation

WORK THIS WEEK (week of 11/14/2022)

- Erosion controls and orange construction fence were completed in the 18 Hole Course
- DiMeo has installed over 300 feet of 36-inch storm sewer on the 18 Hole Course

WORK NEXT WEEK (week of 11/21/2022)

- DiMeo will continue installation of the Little Duke Storage Facility. Delivery of the StormTrap units will continue to use Willow Road for the next several weeks
- DiMeo will continue installing the 36-inch storm sewer overflow pipe in the 18 Hole Course
- Sprinkler heads will be removed on the 18 Hole Course to make way for stormwater improvements

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.

James Bernahl, P.E., Village Engineer: 847-716-3261

JBernahl@winnetka.org

<https://www.villageofwinnetka.org/stormwater>

