


Construction Progress by DiMeo Bros, Inc. (DiMeo)




	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

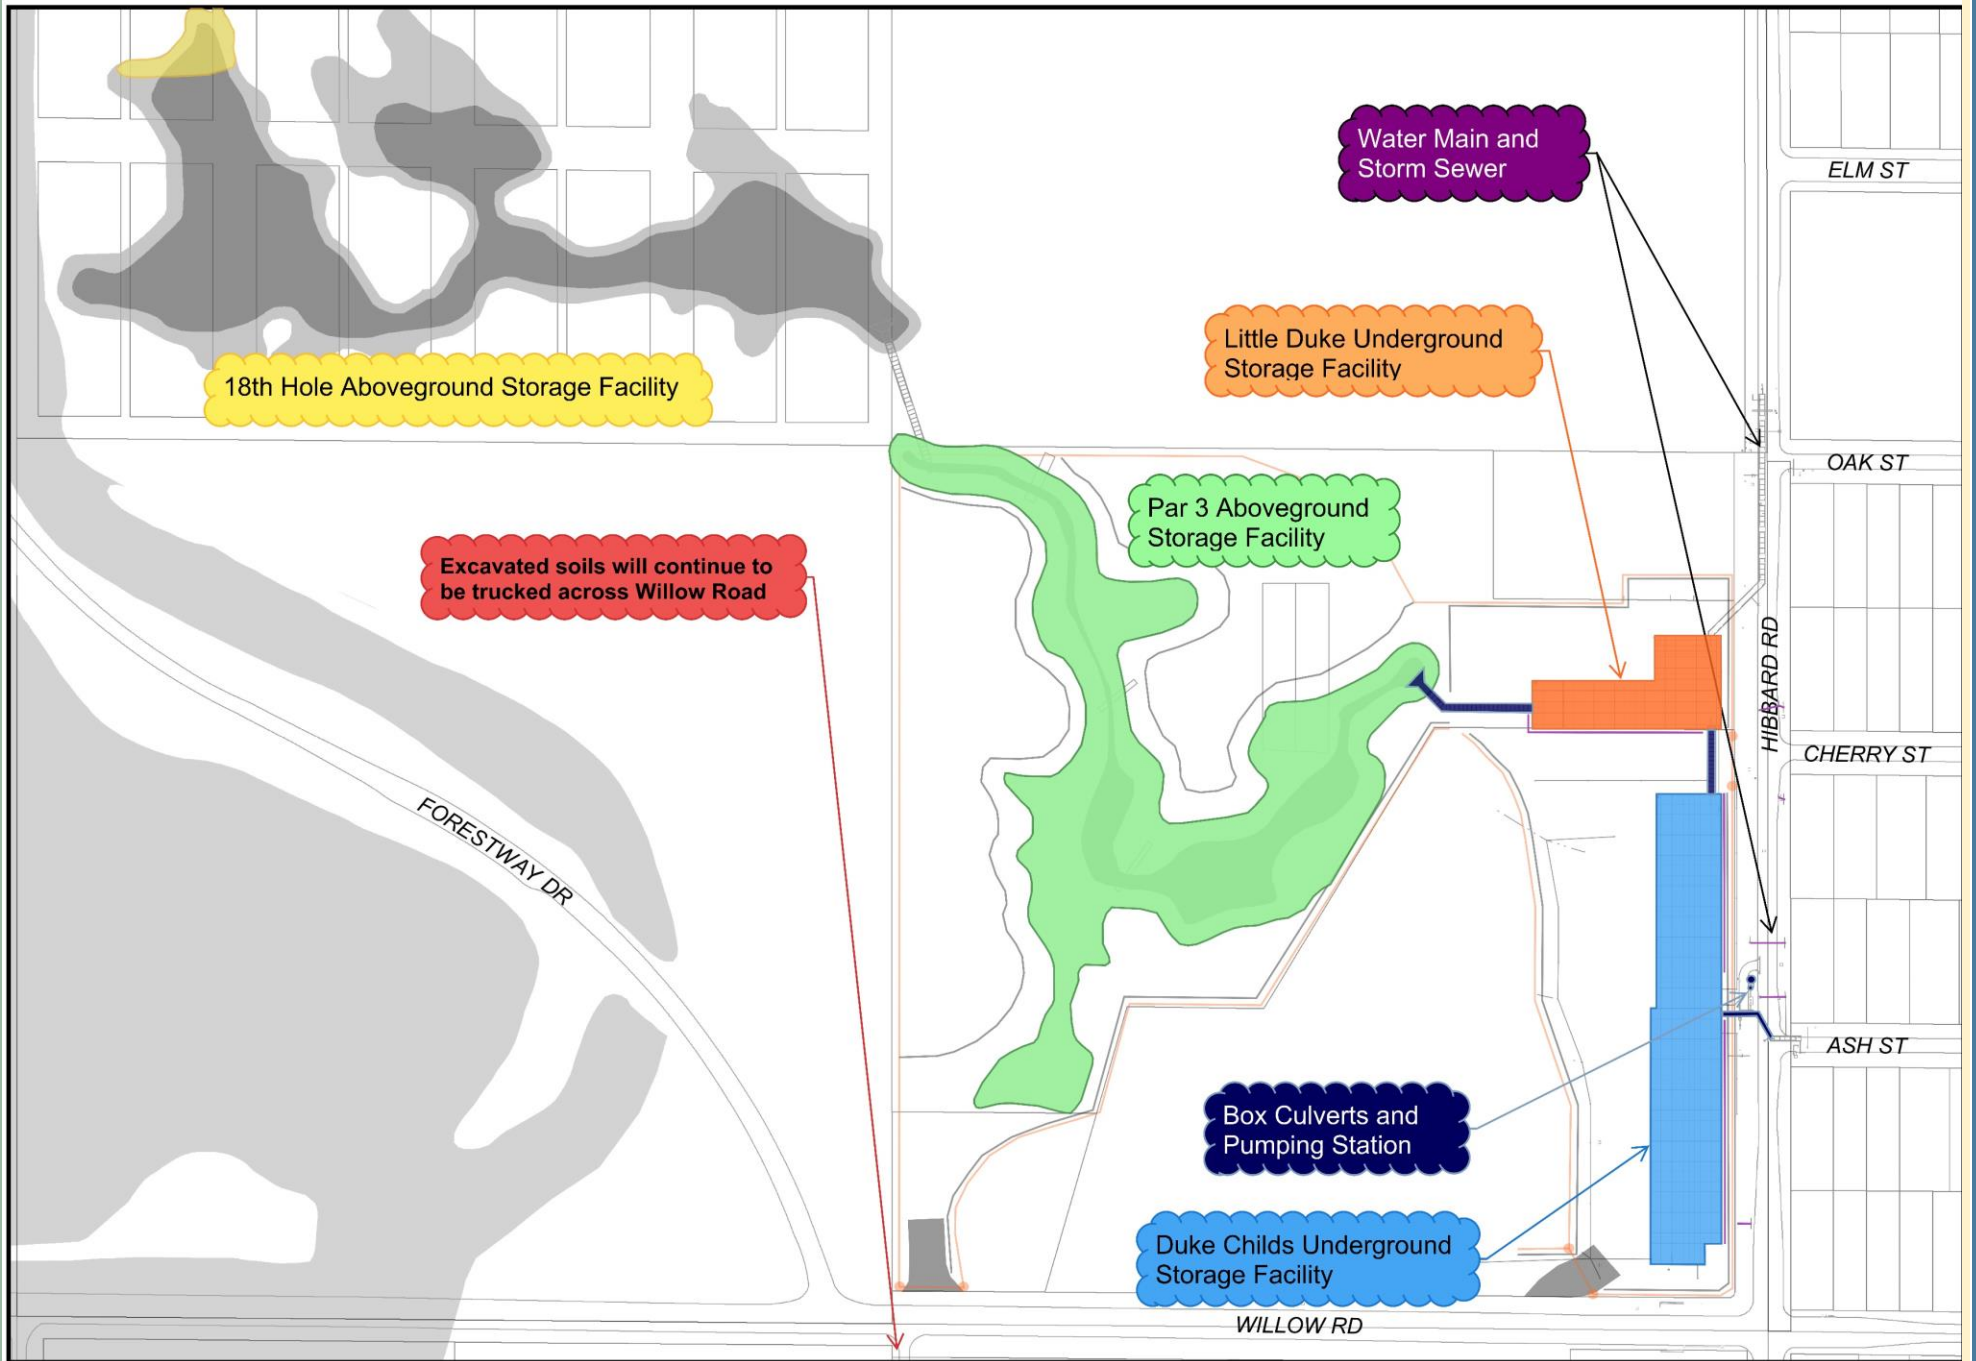

DiMeo began stabilizing the fully-excavated Hole No. 17



Excavation of the 18th Hole Storage Facility has begun!

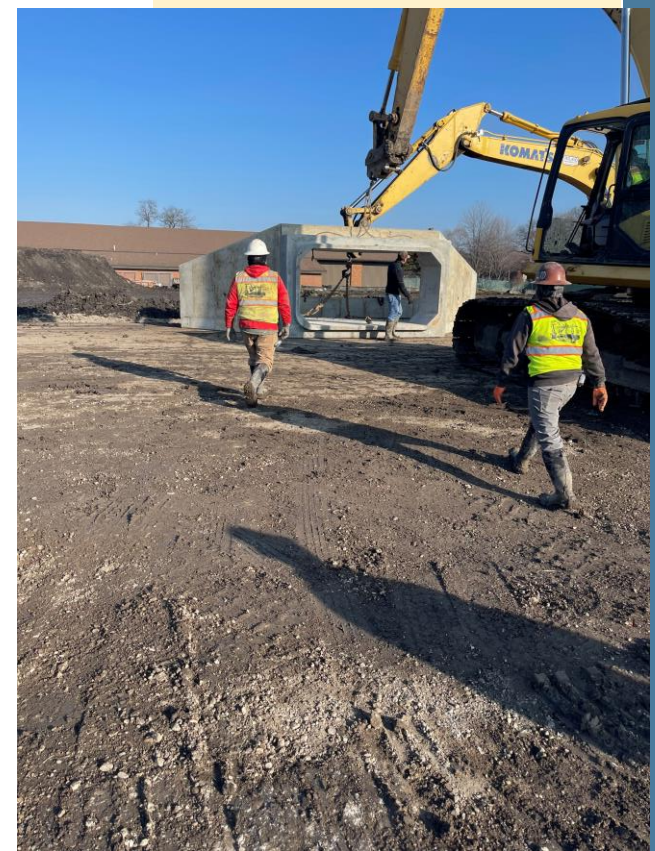

The Par 3 end section will complete the connection with Little Duke

WORK THIS WEEK (week of 1/9/2023)

- DiMeo continued installation of storm sewer and catch basins surrounding Duke Childs and Little Duke
- DiMeo finished excavation of Hole No. 17 and began stabilizing with turf reinforcement mat
- DiMeo began excavation of Hole No. 18

WORK NEXT WEEK (week of 1/16/2023)

- DiMeo will continue installation of local storm sewer on Duke Childs and the Willow Road parking lot
- DiMeo will continue excavation of Hole No. 18 and filling on the northern parts of the golf course
- DiMeo will begin installation of the box culvert from Little Duke to Oak Street

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

