


Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

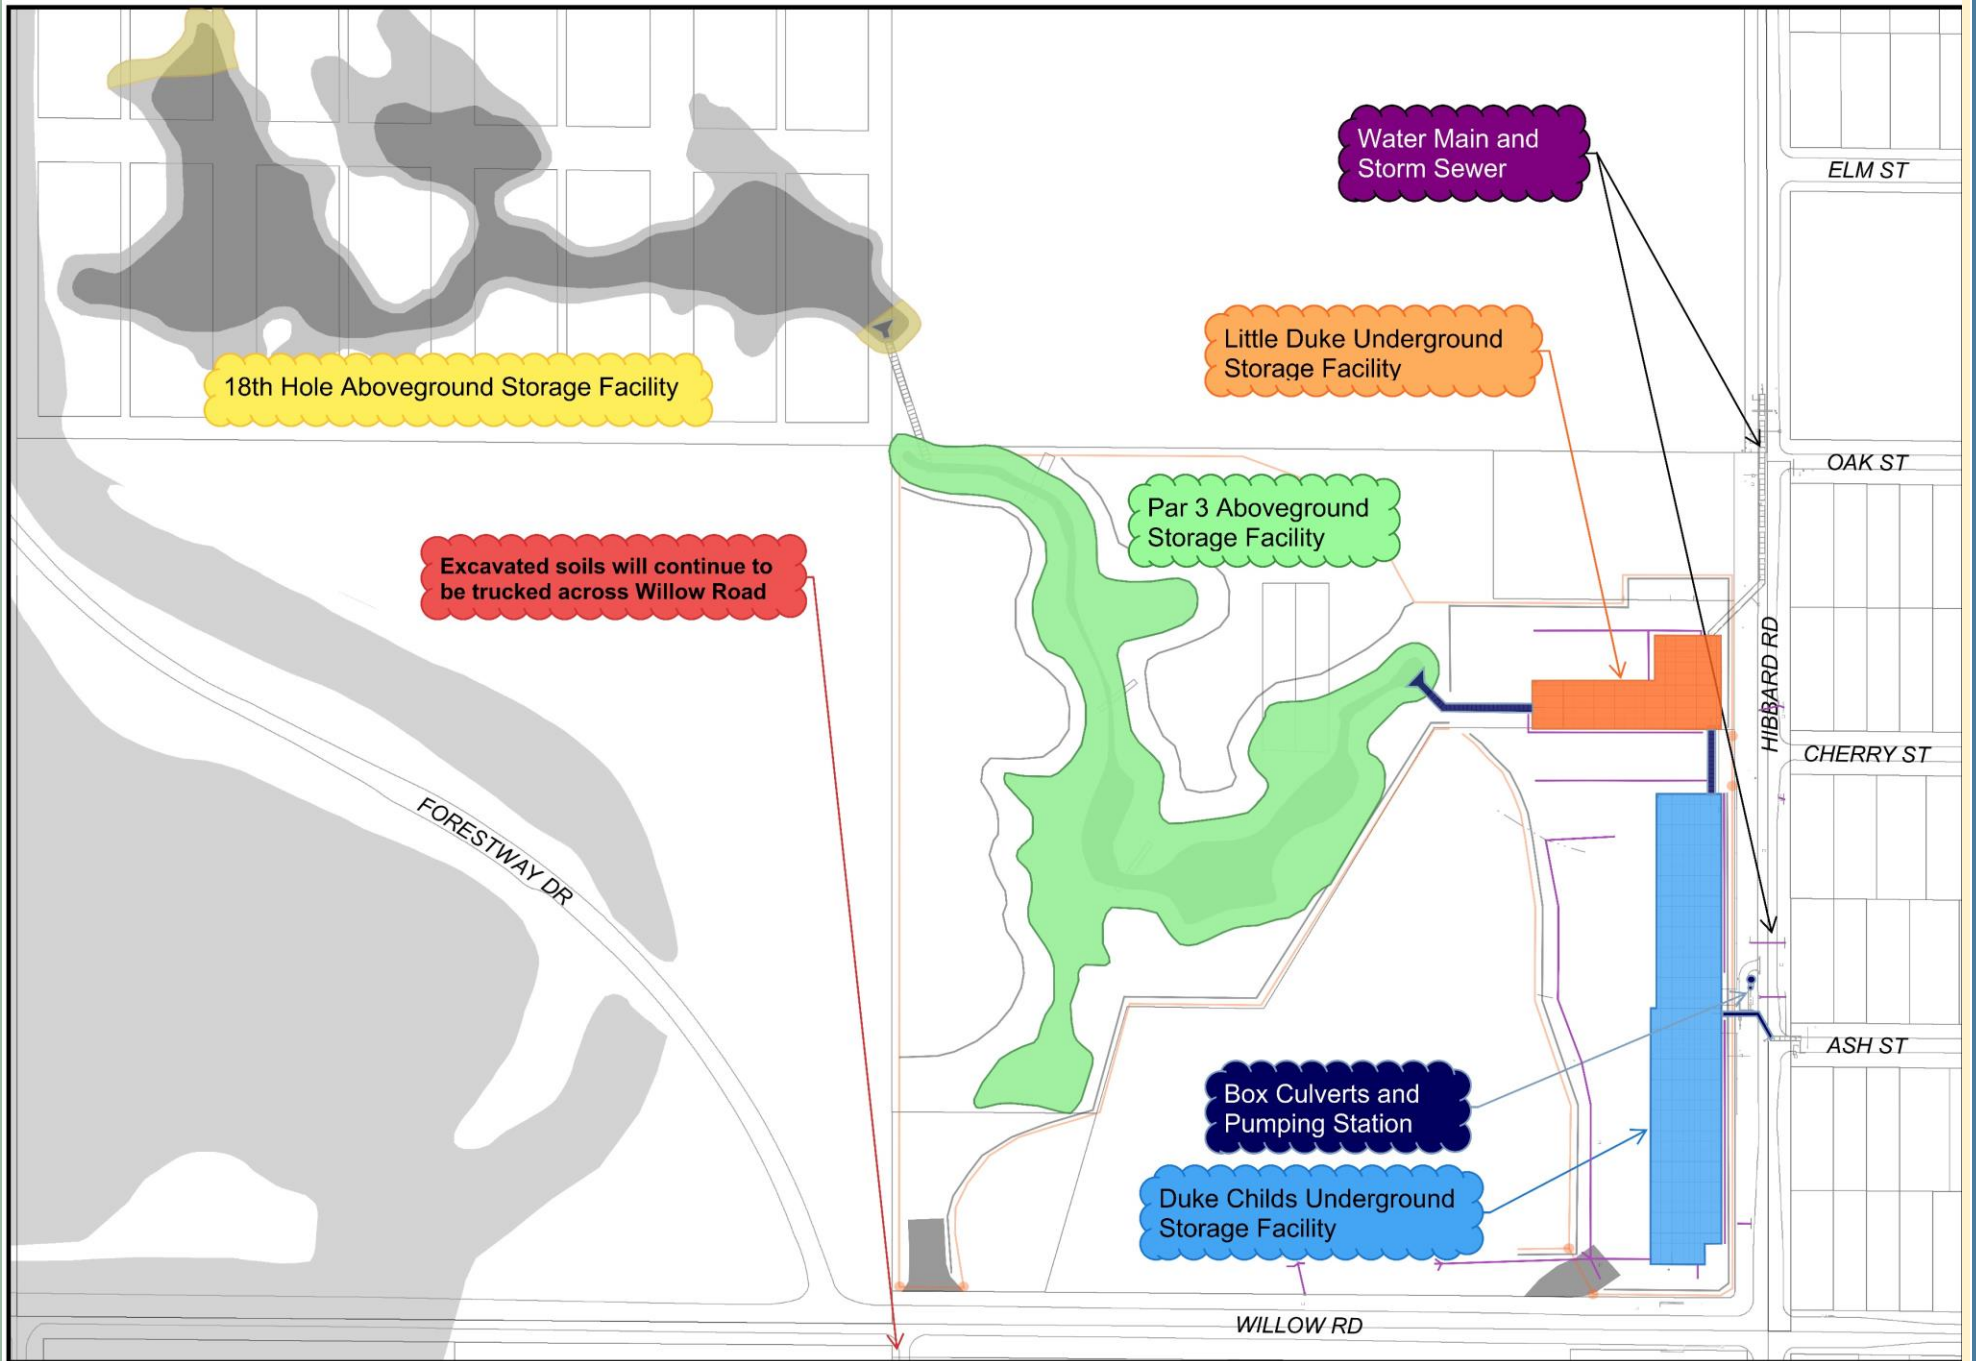

DiMeo began placing topsoil to finished grade on Duke Childs



The first end section connecting the 18th Hole to the Par 3 Course

WORK THIS WEEK (week of 1/23/2023)

- DiMeo continued excavation of Hole No. 18
- DiMeo began installing a large 10'x6' box culvert to connect the 18th Hole to the Par 3 Course
- DiMeo also began removing the haul road on Duke Childs Field, infilling it with topsoil to the finished grade

WORK NEXT WEEK (week of 1/30/2023)

- DiMeo will continue Duke Childs Parking Lot subbase installation and topsoil placement
- DiMeo will continue excavation of Hole No. 18 and filling on the northern parts of the golf course
- DiMeo anticipates completion of the 18th Hole Connecting Culvert between the two golf courses

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

