


Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

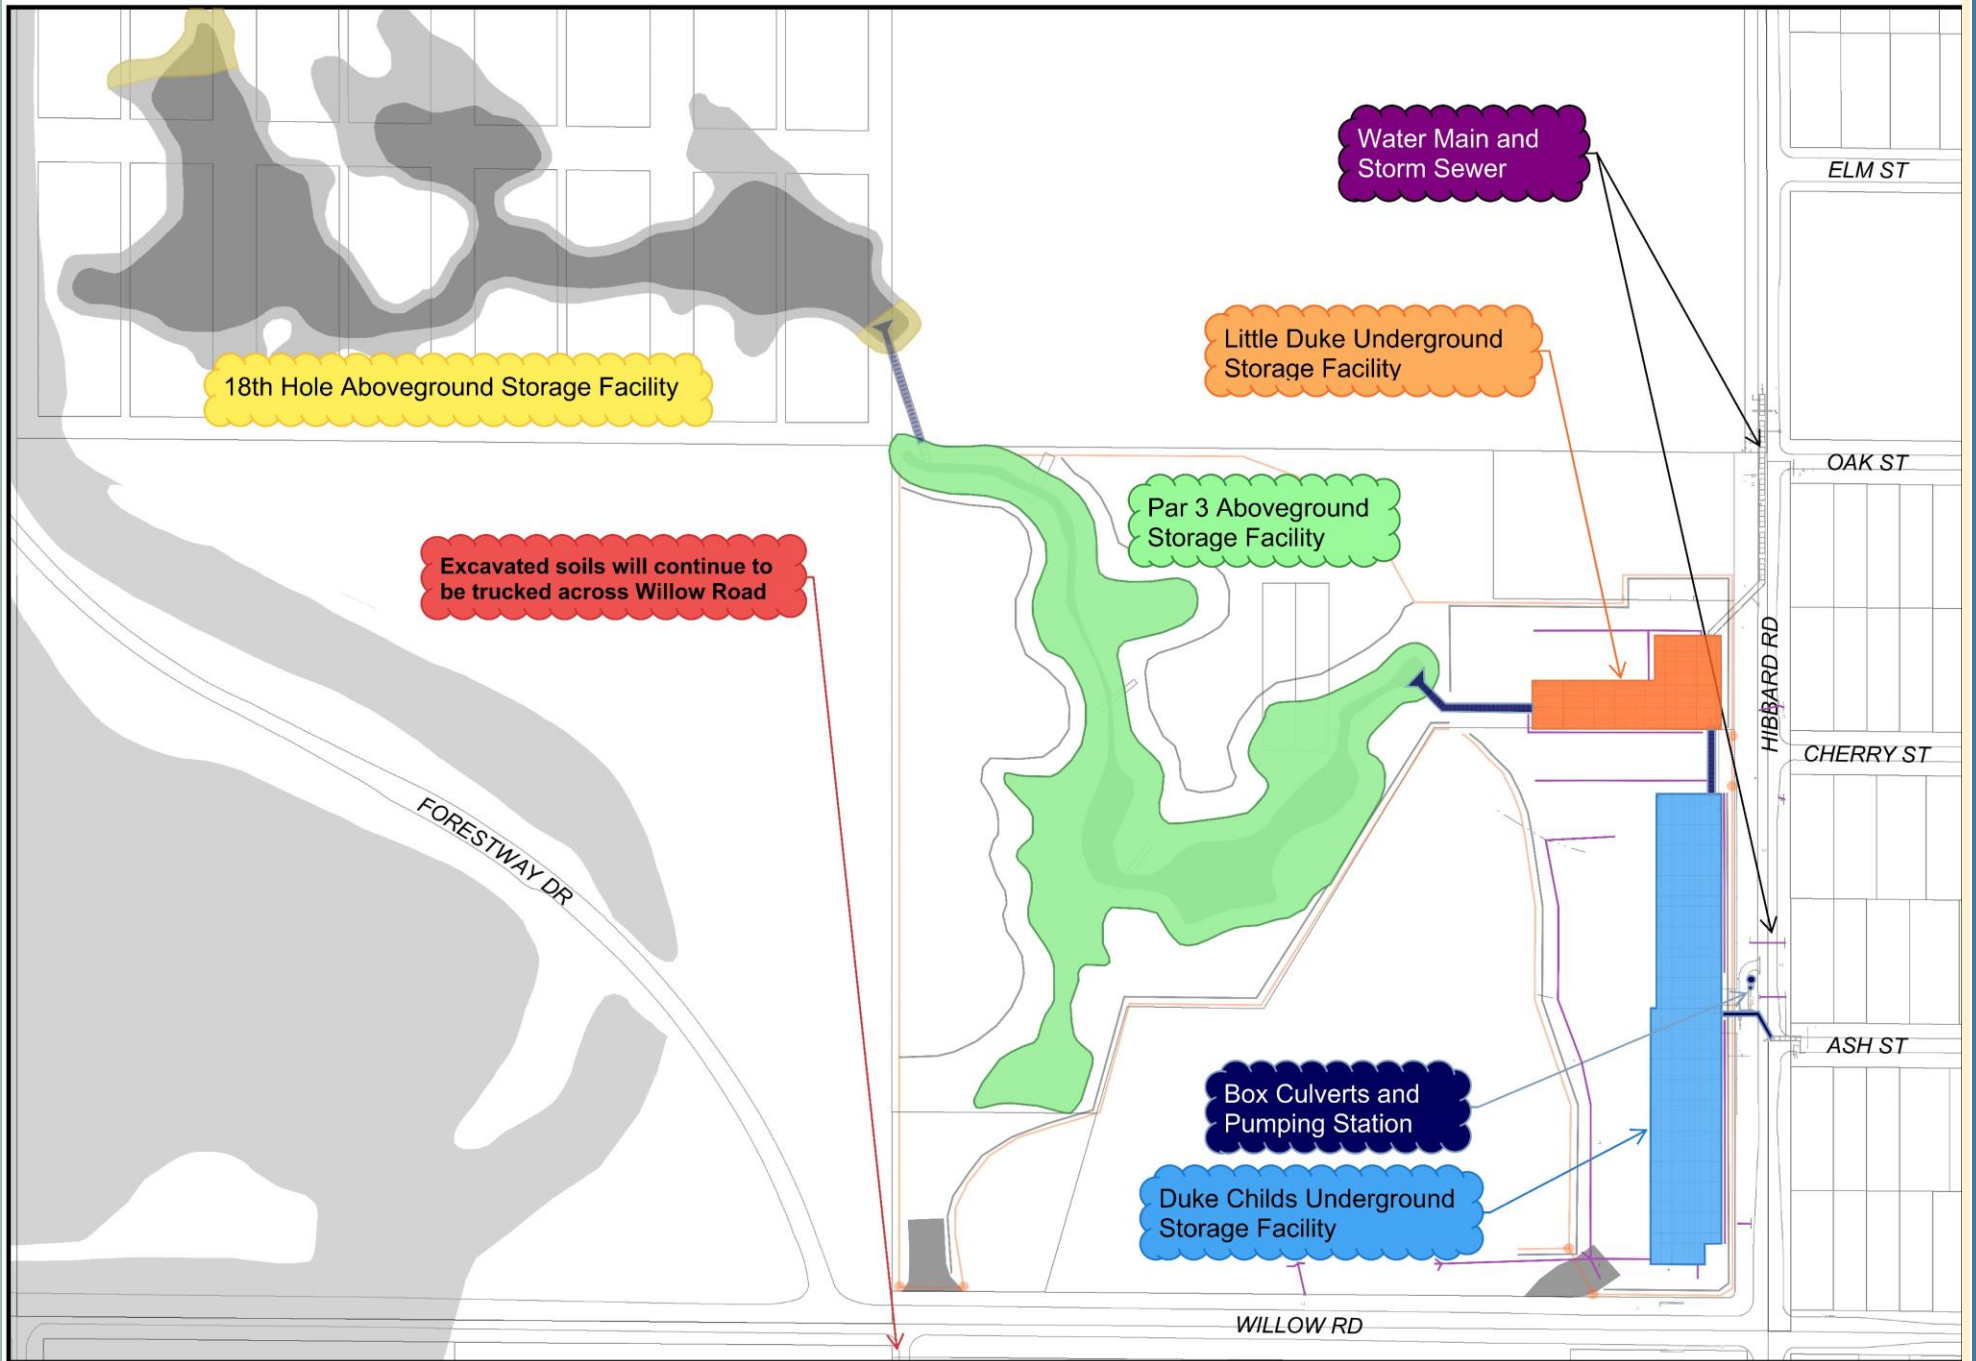

Topsoil placement on Duke Childs Field has been completed



DiMeo rerouted the Winnetka Golf Club sanitary service under the Par 3 Course

WORK THIS WEEK (week of 2/6/2023)

- DiMeo finished adding topsoil to Duke Childs Field to reach the finished grade
- DiMeo installed a new sanitary service to the Winnetka Golf Club clubhouse to avoid conflicts with the Par 3 Storage Facility

WORK NEXT WEEK (week of 2/13/2023)

- DiMeo will pause excavation of Hole No. 18 and filling on the northern parts of the golf course due to the wet conditions
- DiMeo will begin installing the 18th Hole Irrigation Transfer Pumping Station. This station will lift available water from the 18th Hole Storage Facility to the golf course irrigation system.

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

