


### Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

**HIBBARD ROAD TRAFFIC NOTICE:** Hibbard Road will be under one-lane flagger control periodically over the next week. Please be on the lookout for construction workers and consider alternate routes.

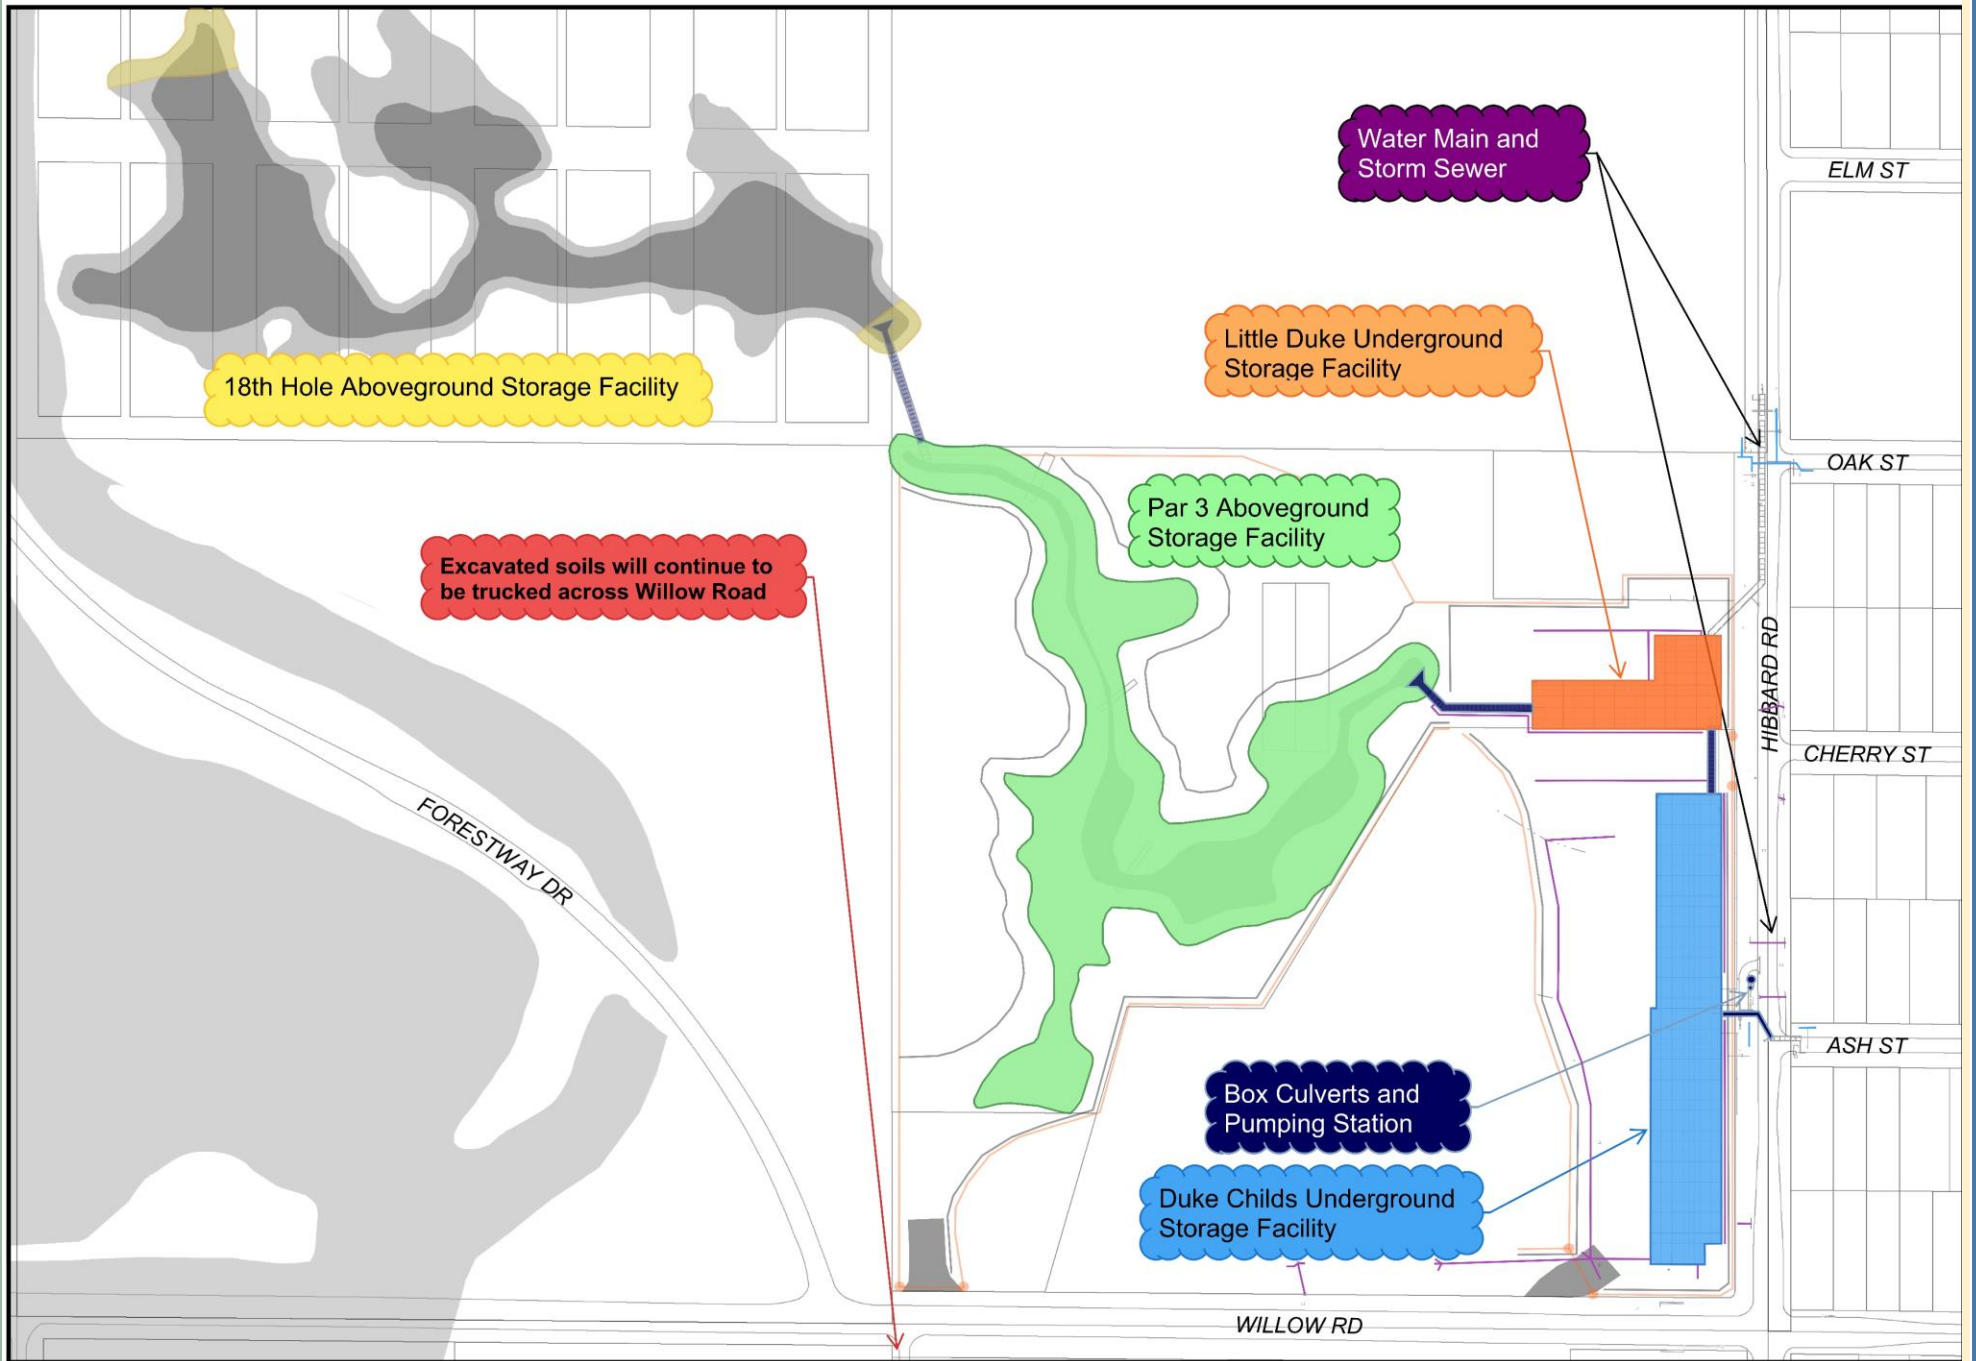

Testing of the previously installed water main occurred this week



DiMeo installed several storm sewers along Oak Street during water main installation

#### WORK THIS WEEK (week of 3/6/2023)

- DiMeo completed pressure testing of the previously installed water main at the intersection of Oak Street and Hibbard Road
- DiMeo completed the haul road to access the 18-Hole Course and Storage Facility

#### WORK NEXT WEEK (week of 3/13/2023)

- DiMeo will make connections between the new water main and the existing water main in the intersection of Oak Street and Hibbard Road
  - **Be on the lookout for message signs indicating the presence of flaggers on Hibbard Road!**
- Bridges on the Par 3 Course will begin to be staked out

#### PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



[JBernahl@winnetka.org](mailto:JBernahl@winnetka.org)



<https://www.villageofwinnetka.org/stormwater>

