


### Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

**HIBBARD ROAD CLOSURE NOTICE:** Hibbard Road will be closed for construction between Willow Road and Elm Street starting on March 25<sup>th</sup> and ending on April 2<sup>nd</sup>. Please follow posted detour routes and use caution while driving in this area.

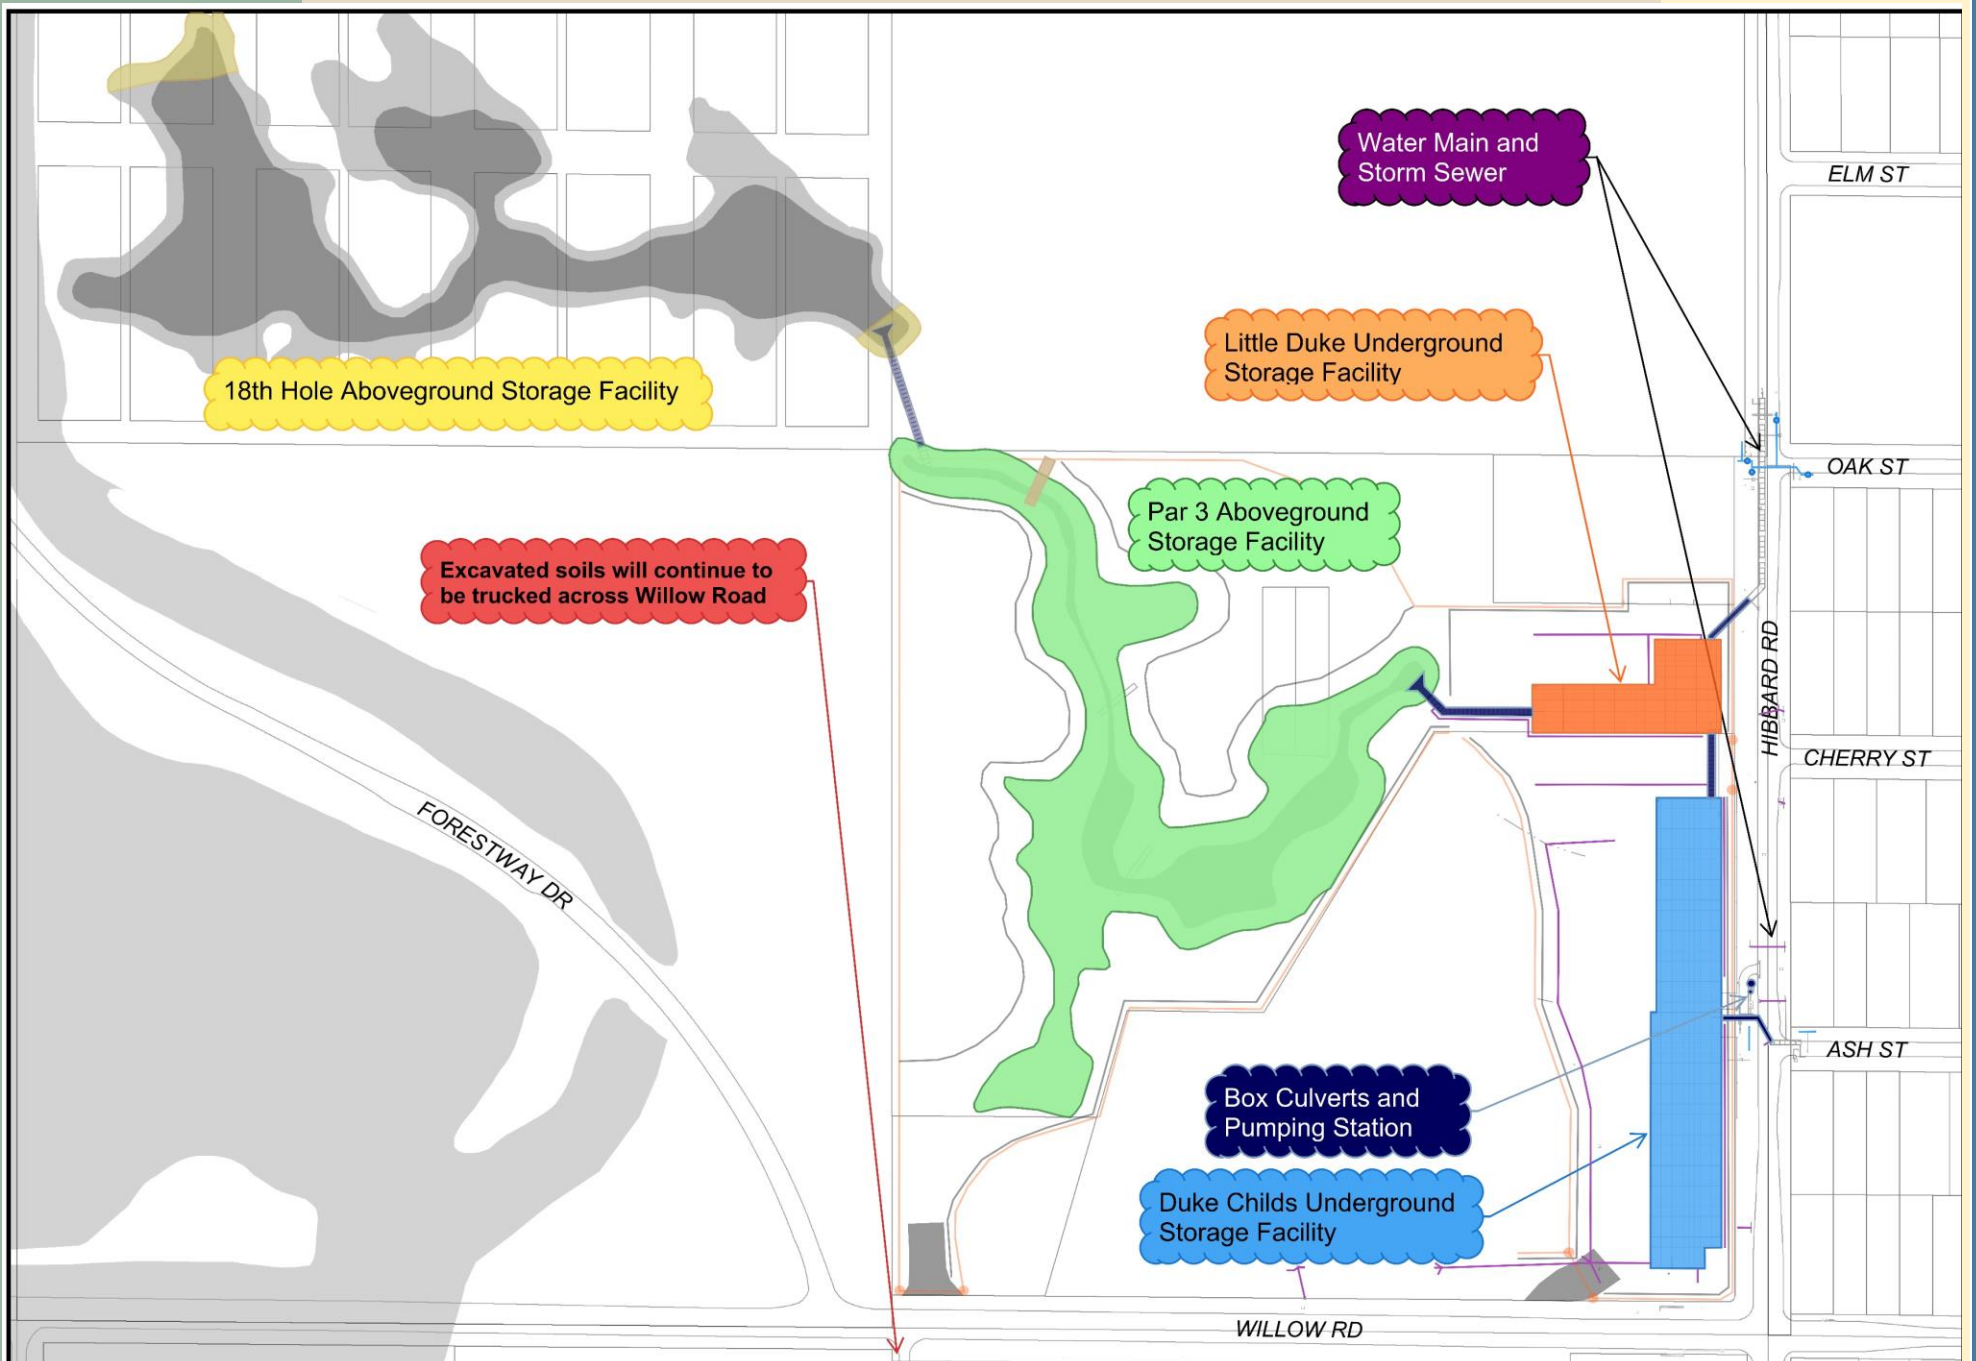

Construction on the first of three Par 3 Course bridges



The Par 3 Course bridges crisscross the 4.6-million-gallon storage facility



DiMeo installs 8'x4' box storm sewers out of Little Duke

#### WORK THIS WEEK (week of 3/20/2023)

- DiMeo completed all water main work near Hibbard Road and Oak Street ahead of storm sewer improvements
- DiMeo continued installing large box storm sewers from the Little Duke StormTrap toward Hibbard Road
- The Bridge Guy, DiMeo's subcontractor, installed the first of three bridges on the Par 3 Course

#### WORK NEXT WEEK (week of 3/27/2023)

- During the Hibbard Road shutdown, DiMeo will install large box storm sewers on Hibbard Road and Oak Street
- The Bridge Guy will continue installing bridges on the Par 3 Course

#### PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



[JBernahl@winnetka.org](mailto:JBernahl@winnetka.org)



<https://www.villageofwinnetka.org/stormwater>

