


### Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

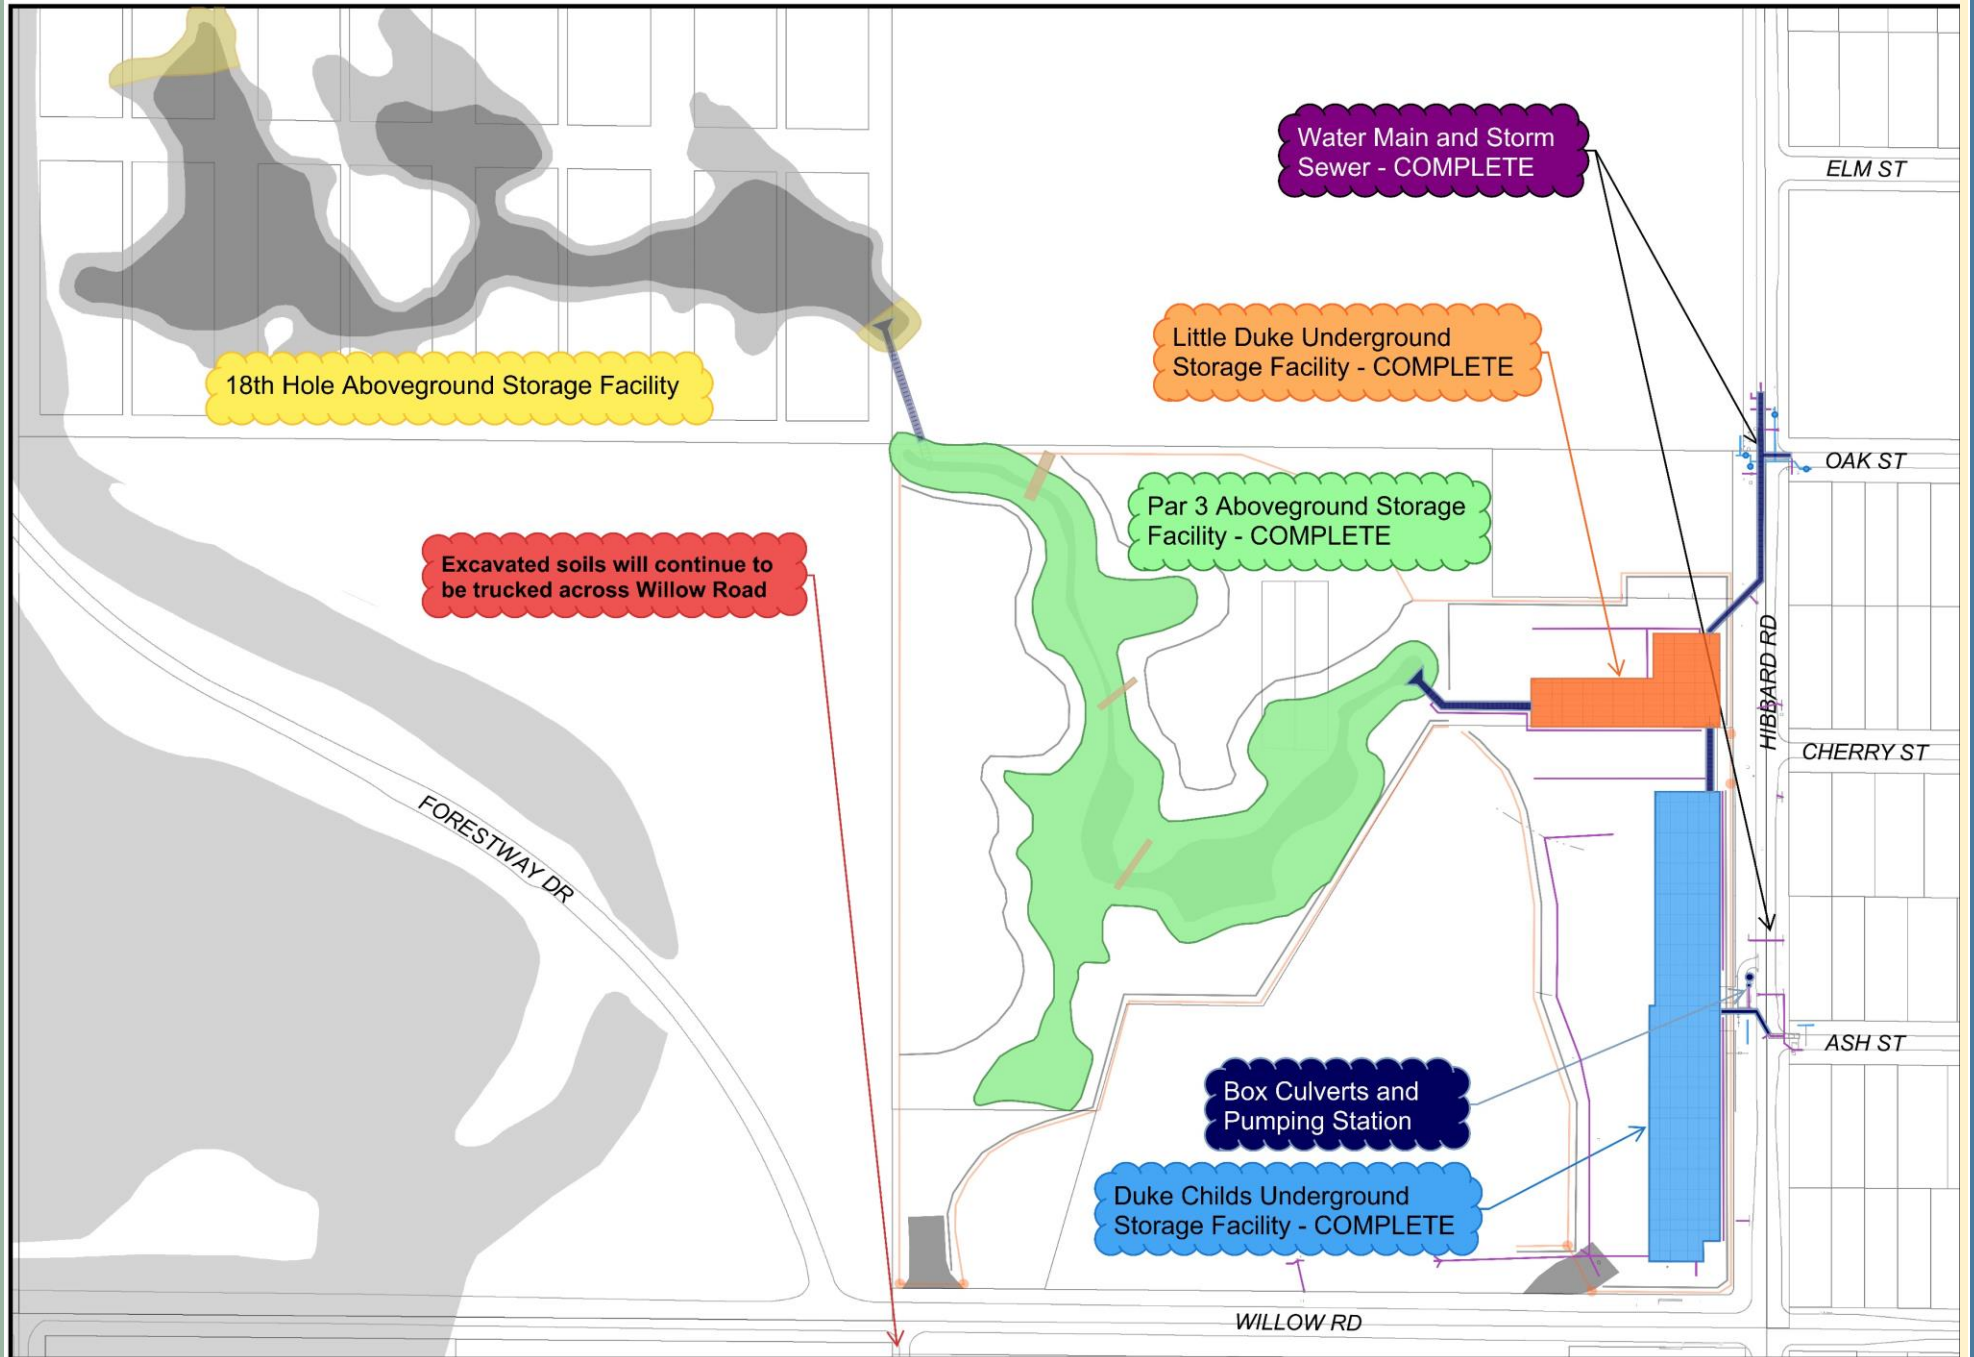

Par 3 bridges are complete



Water levels are down at the culvert connecting Par 3 to Little Duke



The control panel for the renovated Ash Street Pumping Station was relocated

#### WORK THIS WEEK (week of 4/10/2023)

- DiMeo relocated the Ash Street Stormwater Pumping Station control panel to its new location
- DiMeo began restoring parkways on Hibbard Road and Oak Street
- Work on the 18-hole course began in earnest, starting with excavating earth for cart path installation
- Winnetka Park District began applying herbicide to the 18-hole course in preparation for earthwork operations

#### WORK NEXT WEEK (week of 4/17/2023)

- Asphalt plants have **not** opened yet for 2023 paving; however, they might open next week, and restoration of Hibbard Road would then commence
- DiMeo will continue relocating Ash Street Pumping Station equipment to its new location
- Wadsworth, DiMeo's golf course subcontractor, will continue drainage improvements on the 18-hole course
- DiMeo will continue excavating for cart path installation on the 18-hole course

#### PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

