


### Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

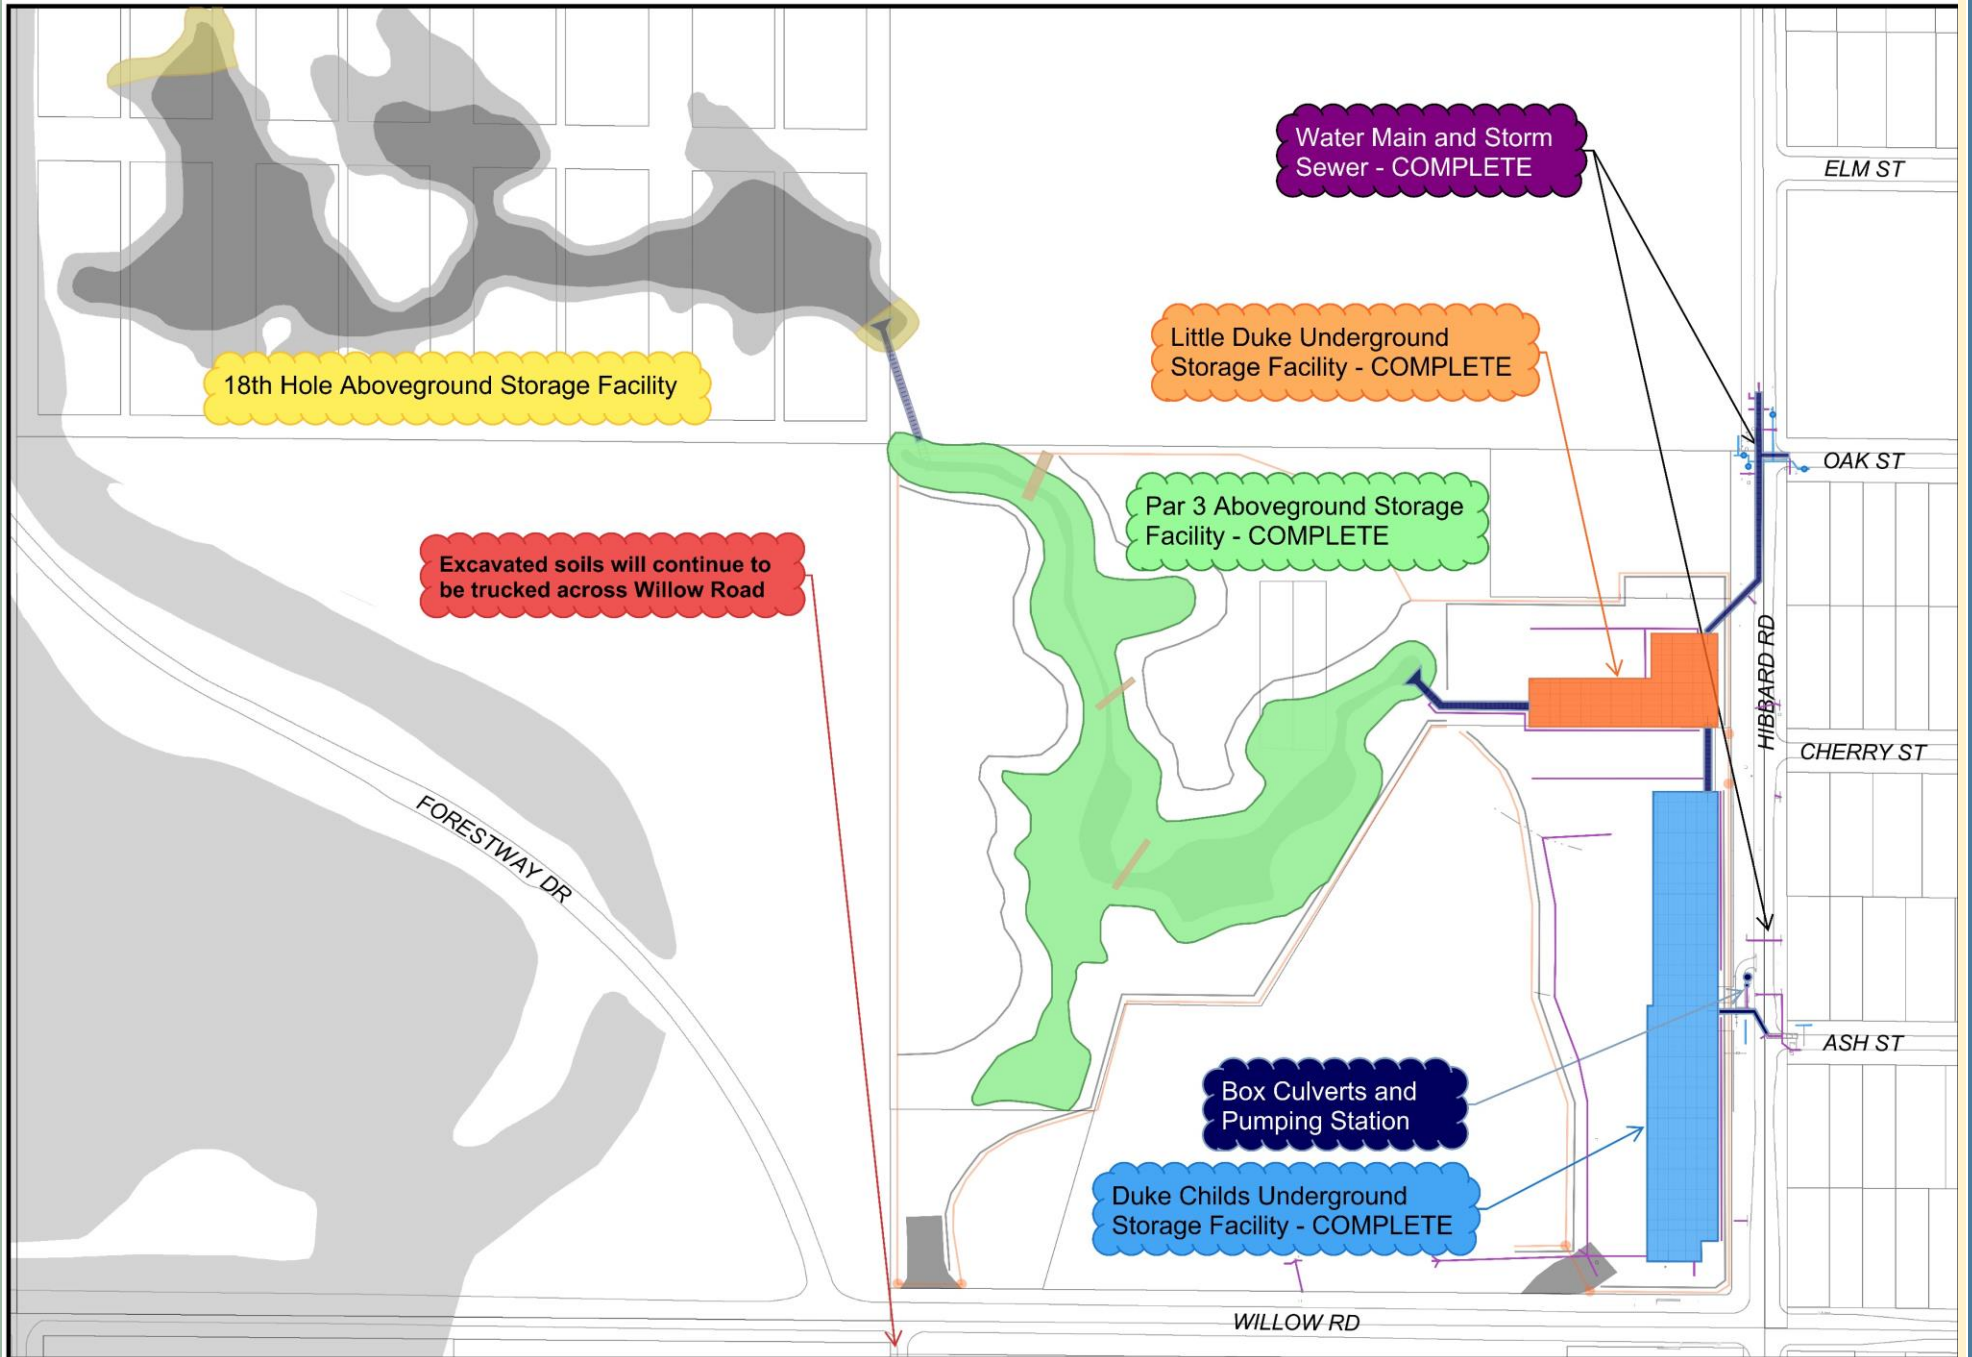

DiMeo's earthmoving equipment in action next to a newly-laid cart path base



Roadway patching began on Hibbard Road. Surface course will be completed next week

Topsoil was stripped and transferred to fill locations on the course



#### WORK THIS WEEK (week of 4/17/2023)

- DiMeo and their subcontractor, Peter Baker & Son, installed hot-mix asphalt patches on Hibbard Road
- DiMeo and Wadsworth Golf Construction continued work on the 18-hole course, laying stone for cart paths, transferring soils, and completing drainage improvements
- The Bridge Guy completed another bridge on the No. 12 hole, making four in total with two left to go this summer

#### WORK NEXT WEEK (week of 4/24/2023)

- Peter Baker & Son will be back to finish restoration of Hibbard Road by laying down an asphalt surface course
- DiMeo will work to restore parkways on Hibbard Road
- Wadsworth will continue drainage improvements throughout the 18-hole course
- DiMeo will continue placing stone for cart paths throughout the 18-hole course and transferring soils to fill locations

#### PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.



James Bernahl, P.E., Village Engineer: 847-716-3261



JBernahl@winnetka.org



<https://www.villageofwinnetka.org/stormwater>

