


Construction Progress by DiMeo Bros, Inc. (DiMeo)



	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23
Par 3 Aboveground Storage Facility															
18th Hole Aboveground Storage Facility															
Duke Childs Underground Storage Facility															
Little Duke Underground Storage Facility															
Hibbard Road Closure															
Water Main and Storm Sewer															
Box Culverts and Pumping Station															
Golf Course and Little Duke Restoration															

WILLOW ROAD TRAFFIC NOTICE: Excavated soils will continue to be trucked across Willow Road causing temporary traffic congestion and increased travel times. Additionally, StormTrap underground units will be delivered onsite via Willow Road. Please consider using alternate routes.

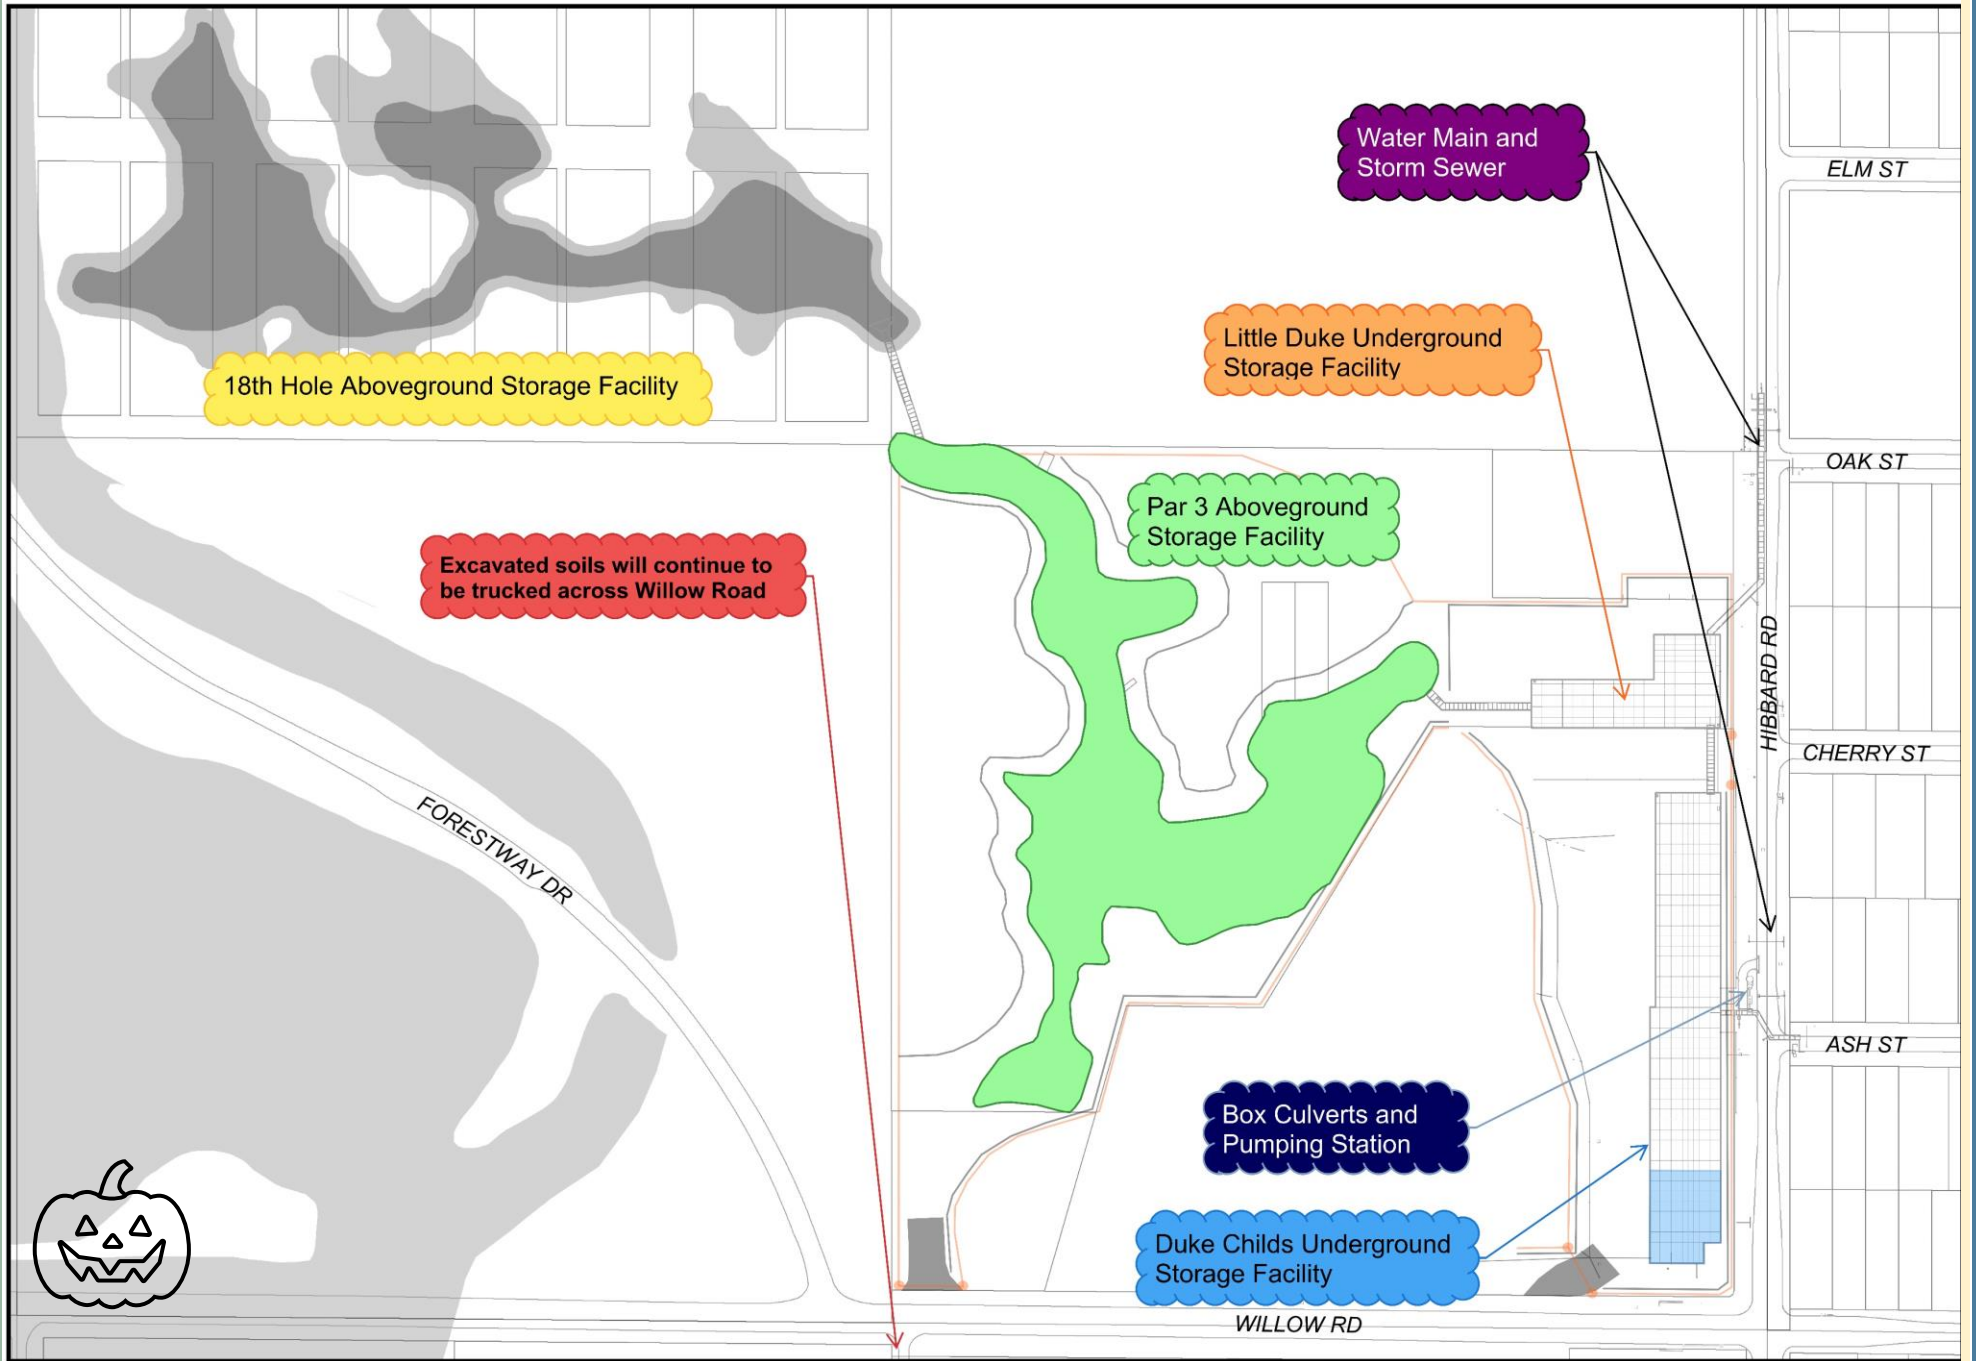

DiMeo continued to install StormTrap units in Duke Childs Field



The Par 3 Channel has been stabilized in time for leaves to fall



WORK THIS WEEK (week of 10/24/2022)

- DiMeo continues to excavate Duke Childs Field and install StormTrap units. They have installed about 25 percent of the 1,142 pieces comprising the Duke Childs Underground Storage Facility

WORK NEXT WEEK (week of 10/31/2022)

- DiMeo will continue excavating Duke Childs Field and installing StormTrap units. Delivery of these units will use Willow Road for the next several weeks
- The Winnetka Golf Club 18 Hole Course will officially close on November 1, making way for the stormwater improvements

PROJECT CONTACT INFORMATION

To be added to the weekly update distribution list, please visit the project website to sign up. For any inquiries, please contact James Bernahl, P.E., Village Engineer, at the contact information listed here.

- James Bernahl, P.E., Village Engineer: 847-716-3261
- JBernahl@winnetka.org
- <https://www.villageofwinnetka.org/stormwater>

